COST BASELINE

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 15, 2026

Time-phased cumulative cost (S-curve) and monthly spend distribution. The cost baseline is direct cost plus contingency reserve. Management reserve sits outside the cost baseline.

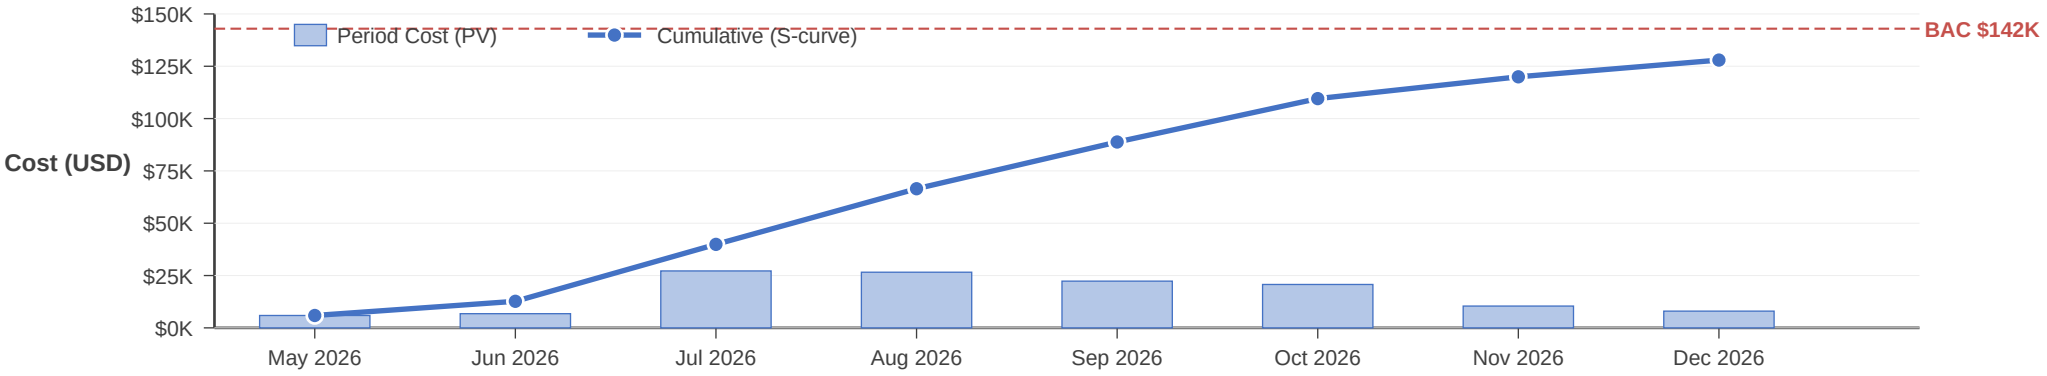

Period	Period Cost (PV)	Cumulative (BAC partial)	% of Direct
May 2026	$5,915	$5,915	4.6%
Jun 2026	$6,775	$12,690	9.9%
Jul 2026	$27,201	$39,891	31.2%
Aug 2026	$26,589	$66,480	52.0%
Sep 2026	$22,327	$88,807	69.4%
Oct 2026	$20,733	$109,540	85.6%
Nov 2026	$10,416	$119,956	93.8%
Dec 2026	$7,996	$127,952	100.0%
Direct Cost Total	**$127,952**	**$127,952**	**100.0%**
+ Contingency Reserve			**$15,000**
= Cost Baseline (BAC)			**$142,952**
+ Management Reserve (sponsor-held)			**$7,500**
= Total Funding Required			**$150,452**
