PROJECT FUNDING REQUIREMENTS

Project Title:	Mary's Consulting – New Company Website	**Date Prepared:**	May 15, 2026

Total funds needed and the timing of when those funds must be available. Funding is released in discrete tranches at the start of each quarter (step function), while expenditures (cost baseline) are incurred continuously throughout the period. The stair-step lies above the S-curve to ensure cash is always available when needed.

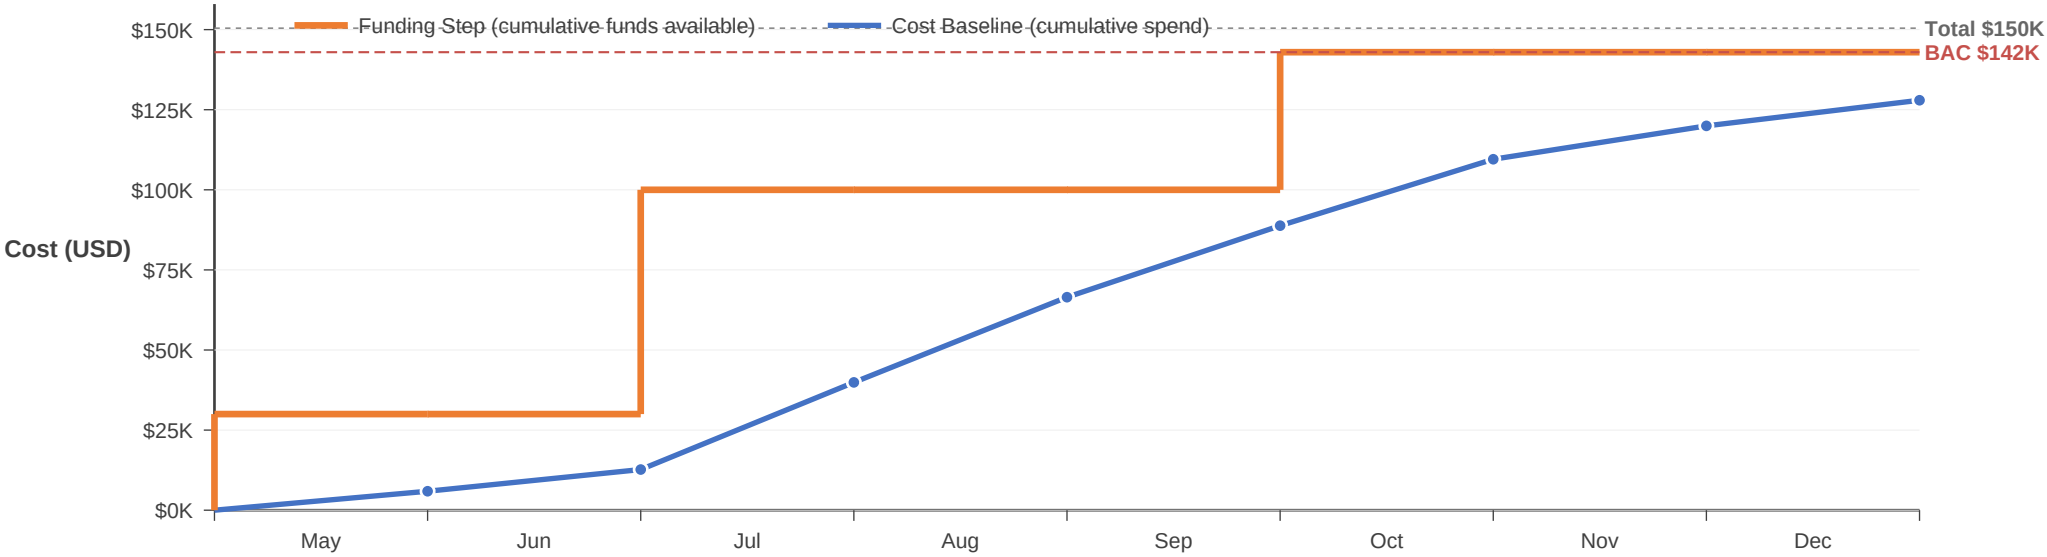

Tranche	Released On	Tranche Amount	Cumulative Funded	Cumulative Spend (Forecast)	Funding Surplus
Tranche 1	May 1, 2026 (start of Q2)	$30,000	$30,000	$12,690	$17,310
Tranche 2	Jul 1, 2026 (start of Q3)	$70,000	$100,000	$88,807	$11,193
Tranche 3 (incl. contingency)	Oct 1, 2026 (start of Q4)	$42,952	$142,952	$127,952	$15,000
Mgmt Reserve (sponsor-held)	Available on request	$7,500	$150,452	$127,952	$22,500
Total Funding Required			**$150,452**		
