PROJECT MANAGEMENT PLAN

Project Management Plan

Comprehensive Plan & Baselines

Project Title:	Mary's Consulting – New Company Website
Project Manager:	Andrew (Project Manager)
Project Sponsor:	Mary (CEO)
Date Prepared:	May 7, 2026
Document Status:	Approved – Baselined
Version:	1.0

CONFIDENTIAL – Internal Use Only | Mary's Consulting © 2026

Project Management Plan – Contents

#	Section	Page
1	Scope Management Plan	3
2	Requirements Management Plan	5
3	Schedule Management Plan	8
4	Financial Management Plan	10
5	Quality Management Plan	13
6	Resource Management Plan	16
7	Communications Management Plan	19
8	Risk Management Plan	21
9	Procurement Management Plan	27
10	Stakeholder Management Plan	30
11	Change Management Plan	34
12	Configuration Management Plan	37
13	Scope Baseline	40
14	Schedule Baseline	50
15	Cost Baseline	52
16	Performance Measurement Baseline	54
17	Project Life Cycle Description	56
18	Development Approach	58

1

Scope Management Plan

Defines how project scope will be defined, validated, and controlled.

SCOPE MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 7, 2026

Work Breakdown Structure (WBS)

The WBS will be developed top-down by the Project Manager with the core team. The project will be decomposed into the following Level 1 deliverables:

1. Project Management
2. Requirements & Design
3. Content Development
4. Build & Integration (CMS, CRM)
5. Test & Quality Assurance
6. Launch & Transition

Each Level 1 deliverable is decomposed to work packages of ≤ 80 hours of effort (8/80 rule). The WBS will be reviewed and approved by the sponsor before the scope baseline is set.

WBS Dictionary

Each work package in the WBS will have a corresponding entry in the WBS Dictionary capturing: WBS code, work package name, description of work, responsible person, deliverables, acceptance criteria, milestones, schedule activities, required resources, cost estimate, and assumptions/constraints. The PM (Andrew) owns the WBS Dictionary and will keep it current with any approved scope changes.

Scope Baseline Maintenance

The scope baseline consists of the approved Project Scope Statement, WBS, and WBS Dictionary. Any change to the baseline requires a written change request approved through the formal Integrated Change Control process. The PM logs all approved changes in the Change Log and updates the baseline. The sponsor (Mary) approves any change that affects scope, cost > $5,000, or the Go-Live milestone.

Deliverable Acceptance

Deliverables are accepted in two stages:

1. Validation: The PM and core team verify the deliverable meets the documented acceptance criteria via internal review and UAT.

2. Formal Acceptance: The Sponsor (Mary) signs the Formal Acceptance Form for each major deliverable. The Marketing Lead signs off on content and brand-related deliverables on behalf of the operational owner.

Final project acceptance is granted at Go-Live with a signed closure document.

Scope and Requirements Integration

Requirements are linked to scope through a Requirements Traceability Matrix (RTM). Each requirement is mapped to one or more WBS work packages and to acceptance criteria, design decisions, and test cases. The RTM is reviewed at each phase gate to confirm that all in-scope requirements are accounted for and that no scope creep has been introduced via unapproved requirements.

2

Requirements Management Plan

Defines how requirements will be analyzed, documented, and managed.

REQUIREMENTS MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 7, 2026

Collection

Requirements will be elicited using interviews with the sponsor (Mary) and key internal stakeholders (Marketing Lead, Sales Lead, IT/Hosting Operations, Legal); facilitated focus groups with Bob, Bill, and Christine; and a written questionnaire distributed to a sample of consultants for content needs. Existing site analytics and competitor reviews will supplement direct elicitation.

Analysis

Each elicited requirement is analyzed for clarity, feasibility, completeness, and alignment with the project charter. Conflicts between stakeholder needs are surfaced early and escalated to the sponsor when they cannot be reconciled by the PM. Requirements failing analysis are rejected or rewritten before they enter the documentation set.

Categories

Requirements are categorized as:

- **Business** – higher-level needs the website must address (e.g., grow F500 leads).
- **Stakeholder** – needs of specific groups (e.g., Marketing's content-edit workflow).
- **Functional** – what the system must do (e.g., RFP form submission).
- **Non-functional** – quality attributes (performance, accessibility, security).
- **Transition** – migration of content from the existing site, training for editors.
- **Project** – constraints on how the project is run (compliance, reporting cadence).

Documentation

Approved requirements are recorded in the Requirements Documentation form with: ID, requirement statement, stakeholder source, category, priority, acceptance criteria, test/verification method, and target phase or release. The PM owns the master document; the team has read access and may propose changes via change request.

Prioritization

Requirements are prioritized using MoSCoW (Must / Should / Could / Won't) by the sponsor with input from Marketing and the PM. Prioritization is set at the close of requirements definition and re-confirmed at each phase gate. Only Must and Should requirements are committed to the launch baseline.

REQUIREMENTS MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 7, 2026

Metrics

The following metrics will be tracked to measure requirements quality:

- % of requirements with documented acceptance criteria (target: 100%)
- Requirements volatility (number of approved changes per month after baseline)
- % of requirements traced to test cases (target: 100% for Must/Should)
- Defects found in UAT traceable to ambiguous requirements (target: < 5% of total defects)

Traceability Structure

A Requirements Traceability Matrix (RTM) is maintained by the PM. Each requirement is traced to: business need, stakeholder, WBS work package, design element, test case, and ultimately a deliverable in the launched website. Forward and backward tracing is supported.

Tracking

Each requirement carries one of these statuses: Proposed, Approved, In Design, In Development, In Test, Verified, Deferred, Rejected. Status is updated weekly during the team's status meeting. The RTM is the single source of truth.

Reporting

Requirements status is reported in the weekly project status report under a 'Requirements Health' section: count by status, approved changes this period, top-3 risks tied to requirements. The full RTM is shared with the sponsor at each phase gate review.

Validation

Each requirement is validated by the requirement's stakeholder source after implementation through UAT or a structured demo. Acceptance is captured as a signed entry on the Formal Acceptance Form. Non-functional requirements (performance, accessibility) are validated through automated testing tools and a third-party WCAG audit before launch.

Configuration Management

Requirements are version-controlled. Once approved, any change requires a written change request that is logged, evaluated for impact (scope, schedule, cost, quality), approved or rejected by the sponsor (or PM, within authority limits), and applied to the baseline. The Change Log records every change with date, requestor, decision, and rationale.

3

Schedule Management Plan

Defines how the schedule will be developed, monitored, and controlled.

SCHEDULE MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 11, 2026

Schedule Methodology

The project will use the **Critical Path Method (CPM)** for schedule development. Activities will be defined from the WBS work packages, sequenced using precedence diagramming (PDM), durations estimated using analogous and expert-judgment techniques, and the schedule baselined after sponsor approval. A predictive (waterfall) life cycle is used overall, with iterative content production within the Content Development phase.

Scheduling Tools

Microsoft Project (firm-standard) is the primary scheduling tool. Schedules will be exported to PDF for stakeholder communication. A simplified milestone view will be maintained in the project status report. Resource availability is tracked in the same tool.

Level of Accuracy

Activity duration estimates will be ±10% during planning and refined to ±5% as the activity nears execution (rolling-wave planning). Contingency reserves of approximately 10% of total duration are held by the PM at the project level for known-unknown risks.

Units of Measure

Activity durations are recorded in **working days** (8-hour days), with effort recorded in **person-hours**. Standard work week is Monday–Friday, U.S. holidays observed. Resources from outside the U.S. (consultants for content) follow their local calendars.

Variance Thresholds

Schedule variance is reported as a percentage of planned duration. Thresholds for action:

- 0–5% behind: monitored, no escalation.
- 5–10% behind: PM develops a corrective-action plan, reports in weekly status.
- > 10% behind, OR any slip to the Go-Live milestone: escalated to the Sponsor (Mary) immediately. Any change to the baseline requires an approved change request.

Schedule Reporting and Format

Weekly: Schedule status section in the project status report — milestones met / missed, upcoming milestones, schedule variance %, top schedule risks.
Monthly: Updated milestone Gantt chart shared with the Sponsor.
Phase Gates: Full schedule review at each phase transition (Design approval, Build complete, UAT complete, Go-Live).

Organizational Procedure Links

This plan aligns with Mary's Consulting's Project Management Office (PMO) procedures: PMO-001 Status Reporting, PMO-007 Integrated Change Control, and PMO-012 Schedule Baselining. The PM will use firm-standard templates for the schedule baseline and milestone reports.

Schedule Updates

Status is collected from team members each Friday and updated in MS Project the same day. The PM reviews the updated schedule, recalculates the critical path, and publishes the weekly status report by end-of-day Monday. The schedule baseline itself only changes through approved change requests; weekly updates reflect actual progress against the baseline.

4

Financial Management Plan

Defines how project costs will be estimated, budgeted, and controlled.

FINANCIAL MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 13, 2026

Units of Measure

All financial figures are in **U.S. dollars (USD)**. Effort is measured in **person-hours**; durations in **working days**. Vendor invoices in foreign currency (if any) are converted at the prevailing rate on the date of approval and recorded in USD.

Level of Precision

Activity-level cost estimates are rounded to the nearest **$100**. Roll-up totals at the work-package, control-account, and project levels are rounded to the nearest **$1,000**. Actuals from accounting are recorded to the cent and reconciled monthly.

Level of Accuracy

Order of Magnitude (-25%/+75%) at charter approval; **Budgetary (-10%/+25%)** at scope baseline; **Definitive (-5%/+10%)** at the cost baseline. The $150,000 charter budget is held as the not-to-exceed limit; the definitive estimate must come in at or below this figure.

Funding Sources

Project funding is sourced from Mary's Consulting's **FY2026 Marketing & Operations capital budget**. All funds are internal — no external financing or co-funding partners are involved. The Sponsor (Mary) is the budget owner and approves the funding allocation.

Funding Frequency & Cash Flow

Funds are released on a **quarterly** basis aligned to expected disbursements (see Funding Strategy for the full S-curve and tranche schedule). The PM provides a 30-day forecast each month so Finance can ensure cash availability ahead of major vendor payments.

Control Thresholds

Cost performance is monitored using earned-value analysis (EVA). Thresholds for action:

- **CV / SV within ±5%** of plan: monitored, no escalation.
- **±5–10%**: PM develops corrective-action plan and reports in weekly status.
- **> ±10%, OR forecast EAC exceeds the $150K cap**: escalated to Sponsor immediately. Any increase to the budget requires an approved change request.

FINANCIAL MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 13, 2026

Rules of Performance Measurement

Earned value is measured at the **work-package level** using these techniques:

- **0/100** for short discrete deliverables (legal pages, training session).
- **50/50** for activities < 2 weeks (most build packages).
- **% complete**, with milestones, for long-running activities (Build Page Templates, Content Production).

Key metrics tracked: PV, EV, AC, CV, SV, CPI, SPI, EAC, ETC, VAC. The PM updates EVA values weekly.

Financial Reporting and Format

Weekly – Cost performance section in the project status report: planned vs. actual spend, CV/SV/CPI/SPI, forecast EAC, top cost risks.
Monthly – Detailed cost reconciliation against Finance system; updated S-curve; cash-flow forecast for the next 90 days.
Phase Gates – Full financial review at each phase gate including projected EAC vs. budget and any required rebaselining.

Reserve Management

Contingency reserve of $15,000 (10% of budget) is held by the PM for known-unknown risks identified in the Risk Register. The PM may release contingency without sponsor approval; usage is reported weekly.
Management reserve of $7,500 (5% of budget) is held by the Sponsor for unknown-unknowns. Use of management reserve requires a formal change request and sponsor approval.

Currency, Tax & Compliance Considerations

All transactions in USD; no foreign-currency hedging required. Vendor payments follow firm's standard accounts-payable terms (Net 30). Any vendor contracts > $25,000 require Procurement and Legal review. SOX-related documentation is preserved per firm's records-retention policy (7 years).

Organizational Procedure Links & Additional Details

Aligns with firm procedures: **FIN-003** Project Cost Coding, **FIN-007** Vendor Invoice Approval, **PMO-007** Integrated Change Control, **PMO-014** Earned Value Reporting. Each work package is assigned a unique project cost code in the Finance system; all actuals are coded at the time of expense capture.

5

Quality Management Plan

Defines quality standards, assurance, and control activities.

QUALITY MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 21, 2026

Quality Standards

The project will adhere to the following standards:

- **WCAG 2.1 Level AA** – Web Content Accessibility Guidelines.
- **Mary's Consulting Brand Standards** (internal) – voice, tone, and visual identity.
- **OWASP Top 10** – web application security best practices.
- **Core Web Vitals** (Google) – LCP, FID, CLS performance thresholds.
- **GDPR** – privacy and consent.
- **Firm SDLC and Code Review policy** (internal).

Quality Objectives

Objective	Metric / Specification – Measure
Accessibility – meet WCAG 2.1 AA on all pages	0 Severity-1 findings in third-party audit
Performance – fast page loads on all device types	75th-percentile LCP < 2.5s on 4G
Defect quality – release with no Sev-1/Sev-2 defects	0 Sev-1, 0 Sev-2 defects open at launch
Content quality – 100% reviewed and approved	100% of pages signed off by Marketing Lead

Quality Roles and Responsibilities

Role	Responsibility
Project Manager (Andrew)	Overall accountability for quality; chairs quality audits; reports quality status to sponsor.
Web Developer / Tech Lead (Bob)	Defect resolution; performance and security testing; code review enforcement.
UX Designer (Bill)	Accessibility compliance; design system quality; visual quality reviews.
Content Strategist (Christine)	Content quality; copy edit; consistency with brand voice; consultant-bio QA.

QUALITY MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 21, 2026

Deliverables and Processes Subject to Quality Review

Deliverables	Processes
• Information architecture / wireframes • Visual design / brand mockups • Page templates & component library • Marketing-page copy & case studies • Consultant directory • Backend APIs & CRM integration • Privacy / cookie / Terms-of-Use pages • Live website at marysconsulting.com	• Requirements elicitation & sign-off • Design review & approval • Code review (peer review on all PRs) • Editorial review of content • Defect logging & triage • Change-control process • UAT & sponsor acceptance • Production cutover & verification

Quality Management Approach

Build quality in — quality is designed in from the start, not inspected at the end. Concretely:

- Accessibility checks built into the component library (not deferred to post-build).
- Automated linting (a11y, performance, code style) on every pull request.
- Editorial review of content as it's written, not after.
- Pair on hard problems rather than review at the end.

Quality Audits conducted at each phase gate (Requirements, Design, Build, Test, Launch) using the firm's Quality Audit form. Findings logged and tracked to closure.

Quality Control Approach

Inspections: Code review on every PR; design review at component-library and template completion; content review at copy completion.
Testing: Automated unit and integration tests run in CI; manual functional tests per the Test Plan; performance and accessibility tests at A030/A031.
Defect Tracking: All defects logged in Jira with severity (Sev-1 to Sev-4) and triaged within 1 business day. Sev-1 / Sev-2 must be resolved before UAT.
Acceptance Criteria: Each deliverable has explicit acceptance criteria (in the RTM); sign-off by the named approver before the deliverable is marked complete.

Applicable Quality Procedures

Firm procedures applied: **QA-001** Code Review Policy; **QA-005** Defect Triage Procedure; **QA-010** Accessibility Review Checklist; **PMO-014** Earned Value Reporting; **SEC-003** OWASP Application Security Review.

6

Resource Management Plan

Defines how resources will be acquired, managed, and released.

RESOURCE MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 17, 2026

Team Member Identification and Estimates


Role	Number	Skill Level
Project Manager	1	Senior
Web Developer / Tech Lead	1	Senior
UX / Visual Designer	1	Mid–Senior
Content Strategist / Copywriter	1	Mid
Frontend Contractor	1	Mid (vendor)
Sponsor / Steering	1	Executive

Staff Acquisition	Staff Release
Core team is sourced internally from existing firm headcount. Functional managers approve allocations. Frontend contractor sourced via firm's approved vendor list with PM signing the SOW. All internal allocations confirmed by May 22, 2026.	Team members are released back to functional managers as their last activity completes. Bill released after accessibility audit (Oct); Christine after CMS training (Nov 24); Bob after hypercare (Dec 10); Andrew at project closeout (Dec 29). Knowledge-transfer documents filed before release.

Roles, Responsibilities, and Authority

Role	Responsibility	Authority
Project Manager (Andrew)	Plan, execute, monitor, and close the project; manage budget, schedule, scope, risks; primary liaison to sponsor.	Approve expenses ≤ $5,000; reallocate budget within 10% of categories; direct core team.
Sponsor (Mary, CEO)	Authorize project; approve charter, baselines, and changes; approve brand direction; provide funding.	Final approval on charter, scope/cost/schedule changes exceeding PM authority, brand decisions, project closure.
Web Developer (Bob)	Lead technical architecture, CMS configuration, frontend/backend development, CRM integration.	Owns technology stack decisions in consultation with PM; approves dev/staging/prod environment changes.
UX Designer (Bill)	Information architecture, wireframes, visual design, accessibility compliance.	Owns design system decisions; signs off on accessibility audit findings.
Content Strategist (Christine)	Content strategy, page copy, case studies, blog seed, consultant bio coordination.	Owns editorial standards; approves content from consultant submissions.
Marketing Lead	Internal stakeholder; approves brand fit, content tone, launch plan; owns site post-launch.	Approves content/brand alignment; final acceptance of marketing-related deliverables.

Project Organizational Structure



RESOURCE MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 17, 2026

Training Requirements

- **Marketing team:** 4-hour CMS training session held the week of launch; quick-reference guide delivered.
- **Bob (Dev):** No new training required; current skills cover the stack.
- **Bill (UX):** WCAG 2.1 AA refresher (self-paced) completed before design phase.
- **Christine (Content):** Brand-voice workshop with Marketing Lead before content production starts.

Rewards and Recognition

- Project completion bonus pool ($3,000) administered by the PM at closeout, allocated based on contribution.
- Public recognition at the firm's all-hands meeting after launch; Mary to highlight team contributions.
- Spot recognition at weekly status meetings for exceeding-expectations work.
- Consultants featured in case studies receive named credit on the new website.

Team Development

- **Forming → Storming → Norming → Performing:** PM actively manages team-development through Tuckman's stages, with extra coaching during the design phase where creative tensions are most likely.
- **Team charter** developed in week 1 covering working agreements, communication norms, and decision rights.
- **Weekly retrospectives** during build phase; monthly otherwise.
- **Co-location:** Hybrid model with one in-person team day per week during the build phase to support design/dev hand-offs.

Physical Resource Identification and Estimates

Resource	Amount	Grade
Cloud hosting (dev/staging/prod)	3 environments	Firm-approved cloud provider; standard tier
CMS license (annual)	1 seat group	Firm-approved CMS; supported tier
CI/CD pipeline access	1 project	Firm-standard tooling
Stock imagery library	~50 images	Royalty-free, commercial license
Photography session	1 day	External photographer; consultant headshots
WCAG 2.1 AA audit (3rd party)	1 audit cycle	Accredited accessibility firm
Analytics & monitoring tools	1 setup	Google Analytics, tag manager, uptime monitoring
Project tools (MS Project, etc.)	Existing licenses	Firm-issued

Resource Acquisition	Resource Management
Cloud and CMS resources acquired via existing firm agreements (no new contracts). Stock imagery and photography purchased per a single vendor SOW signed by the PM. WCAG audit awarded via competitive bid (3 quotes; lowest-cost qualified vendor). All vendor SOWs stored in the project SharePoint.	Resource utilization tracked weekly by the PM in MS Project. Cloud spend reviewed monthly against forecast. Imagery licenses inventoried at content approval and closeout. All physical resources listed in this plan are project-owned for the project's duration; hosting transitions to IT/Hosting Operations ownership at handoff (Dec 15).

7

Communications Management Plan

Defines who needs what information, when, and how it will be delivered.

COMMUNICATIONS MANAGEMENT PLAN

Project Title: Mary's Consulting Corporate Website Redesign **Date Prepared: May 6, 2026**

Stakeholder	Information	Method	Timing or Frequency	Sender
Mary (CEO / Sponsor)	Project status, schedule & budget variance, key risks, milestone progress	Email + Executive briefing (video call)	Bi-weekly; ad hoc for escalations	Andrew (PM)
Project Team — Bob, Bill, Christine	Task assignments, daily progress, blockers, design decisions	Daily stand-up (video) + Slack channel	Daily (15 min stand-up)	Andrew (PM)
Project Team — Bob, Bill, Christine	Sprint review, retrospective, sprint planning	Video conference (Zoom)	Bi-weekly (end of each 2-week sprint)	Andrew (PM)
Consultant Community (500+ end users worldwide)	Launch updates, feature previews, training resources, go-live notice	Company-wide email newsletter + intranet post	Monthly during build; weekly leading up to launch	Andrew (PM) on behalf of Mary
Web Development Vendor	Requirements, design specs, change requests, acceptance criteria	Email + shared project management tool (Jira)	Weekly status; ad hoc for change requests	Andrew (PM)
All Stakeholders	Major milestone announcements, go-live communication, post-launch results	Formal email + town-hall meeting	At each milestone (Charter approval, Design sign-off, UAT, Launch)	Mary (Sponsor) / Andrew (PM)
Mary (CEO / Sponsor)	Formal Project Status Report (cost, schedule, scope, risk dashboard)	Written report (PDF) attached to email	Monthly	Andrew (PM)

Assumptions	Constraints
• All stakeholders have access to corporate email and the company Slack workspace. • Team members (Bob, Bill, Christine) are available during agreed core overlap hours despite being globally distributed. • English is the primary communication language for all project artifacts. • The web development vendor will follow Mary's Consulting communication protocols. • Mary will be available for monthly status reviews and milestone sign-offs.	• Time-zone differences across 500+ consultants worldwide limit synchronous communication windows. • Confidentiality requirements for Fortune 500 client data restrict what may be shared on the public-facing website. • Bandwidth limitations in some consultant regions may affect video conferencing quality. • Sponsor (Mary) availability is limited to scheduled meetings only. • Project budget caps the use of paid communication tools to existing licenses.

Glossary of Terms or Acronyms

PM – Project Manager | **CEO** – Chief Executive Officer | **UAT** – User Acceptance Testing | **MVP** – Minimum Viable Product
SoW – Statement of Work | **KPI** – Key Performance Indicator | **CMS** – Content Management System | **SEO** – Search Engine Optimization
RACI – Responsible, Accountable, Consulted, Informed | **RFP** – Request for Proposal | **SLA** – Service Level Agreement

8

Risk Management Plan

Defines how risks will be identified, analyzed, and responded to.

RISK MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 19, 2026

Strategy
The project will use a **balanced risk strategy**: actively identify and mitigate threats that could impair the November 2026 Go-Live, while pursuing a moderate appetite for opportunities that improve scope or schedule. Risk responses are integrated into project planning rather than treated as a separate workstream.

Methodology
Risk management follows the PMBOK 8th-edition risk process: Plan → Identify → Analyze (qualitative + quantitative as needed) → Plan Responses → Implement Responses → Monitor. Tools include brainstorming, interviews, root-cause analysis, SWOT, the Risk Breakdown Structure (below), and a 5×5 Probability and Impact Matrix. The Risk Register is the master artifact.

Roles and Responsibilities

Role	Responsibility
Sponsor (Mary)	Owns project-level risk acceptance; approves use of management reserve; tolerates / escalates strategic risks.
Project Manager (Andrew)	Owns risk-management process; maintains Risk Register; facilitates identification & analysis; allocates contingency.
Risk Owners (per risk)	Each individual risk has a named owner (usually a team member); responsible for executing the response plan and reporting status.
Team Members (Bob, Bill, Christine)	Identify domain-specific risks; implement mitigations within their domain; raise emerging risks at weekly standup.

RISK MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 19, 2026

Risk Categories – Risk Breakdown Structure (RBS)

Hierarchical decomposition of risk sources for the project. Used during identification to systematically scan each category.



Risk Management Funding

Contingency reserve: $15,000 (≈10% of direct estimate) is held by the PM, allocated specifically to known risks identified in the Risk Register. The PM may release contingency without sponsor approval; usage is reported weekly.
Management reserve: $7,500 (≈5%) held by the Sponsor for unknown-unknowns. Use requires a formal change request and sponsor approval.
Risk-management activities themselves (facilitation, analysis, register maintenance) are absorbed in PM hours, not separately funded.

Contingency Protocols

- Contingency is allocated to specific risks in the Risk Register, not pooled.
- When a risk materializes, the PM may execute the documented response and draw against the contingency line item without further approval.
- Drawing > $5,000 in a single event triggers an immediate sponsor notification (not approval — notification only, since the funds were pre-approved).
- Unused contingency at project close is returned to the firm's general budget; it does **not** roll into scope expansion.

RISK MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 19, 2026

Frequency and Timing

Identification: Continuous; formal review at the start of each phase (kickoff, design, build, test, launch, closeout).
Analysis: Newly identified risks analyzed within 5 business days.
Response planning: Mitigation plans drafted within 10 business days of identification for High and Critical risks; 20 days for Medium.
Monitoring: Top 5 risks reviewed at every weekly team standup; full Risk Register reviewed monthly with the Sponsor.
Audit: Formal Risk Audit at each phase gate to validate that risk responses are working and that the process itself is effective.

Stakeholder Risk Tolerances

Sponsor (Mary): Low tolerance for budget overrun (any spend > $150K cap requires formal approval). Medium tolerance for schedule slip (≤ 2 weeks acceptable). Zero tolerance for accessibility or security non-compliance.
Marketing Lead: Low tolerance for content-quality compromises; will accept timeline delay over publishing below-standard content.
IT / Hosting Operations: Zero tolerance for production stability risks; demands rollback plan for every cutover.
Legal / Compliance: Zero tolerance for GDPR or WCAG findings; escalates immediately.
PM: Authority to accept risks with combined exposure ≤ $5,000 without sponsor approval.

Risk Tracking and Audit

All risks are tracked in the Risk Register with a unique ID, category (per RBS), description, probability, impact, score, owner, response strategy, and status (Open / Mitigating / Closed / Realized). The Risk Register is version-controlled in the project SharePoint. A Risk Audit (using the firm's Risk Audit form) is conducted at each phase gate; findings are logged in the Lessons Learned Register.

RISK MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 19, 2026

Definitions of Probability

Level	Probability Range	Description
Very High	> 70%	Almost certain to occur within the project timeframe.
High	50% – 70%	More likely than not to occur.
Medium	30% – 50%	Reasonable chance of occurrence.
Low	10% – 30%	Unlikely but plausible.
Very Low	< 10%	Improbable; only worth tracking if impact is severe.

Definitions of Impact by Objective


Level	Scope	Quality	Time	Cost
Very High	Loss of major deliverable	Unacceptable to sponsor	> 4-week slip	> $15,000
High	Major scope reduction	Major quality degradation	2–4 week slip	$7,500 – $15,000
Medium	Significant change required	Quality requires sponsor review	1–2 week slip	$3,000 – $7,500
Low	Minor scope adjustment	Quality acceptable to sponsor	< 1 week slip	$1,000 – $3,000
Very Low	Trivial / no scope impact	No noticeable quality impact	Days only	< $1,000

RISK MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 19, 2026

Probability and Impact Matrix

Each risk is scored as Probability × Impact (1–5 scale). Higher scores demand more aggressive responses and earlier escalation.

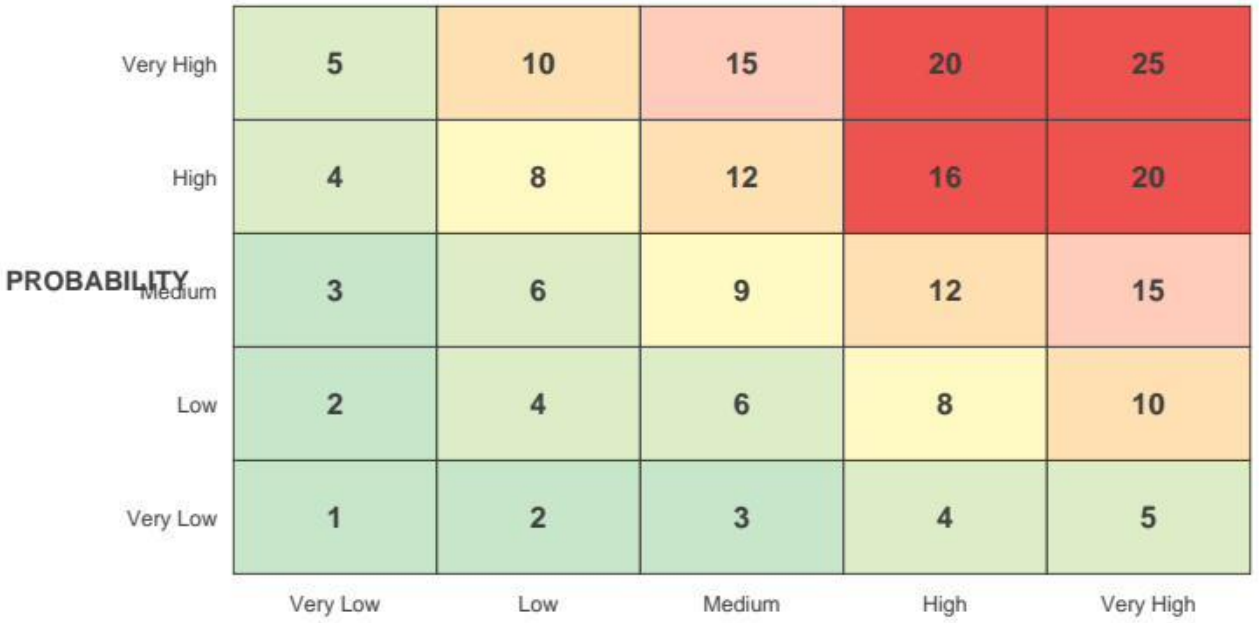

Score	Risk Level	Required Response
16 – 25	Critical	Active mitigation required; escalate to sponsor immediately; weekly status to PM.
13 – 15	High	Mitigation plan documented within 10 days; weekly tracking; PM-managed contingency.
10 – 12	Medium-High	Mitigation plan within 15 days; bi-weekly tracking.
7 – 9	Medium	Mitigation plan within 20 days; monthly tracking.
4 – 6	Low	Monitor; respond if conditions change.
1 – 3	Very Low	Watchlist only; no action unless impact increases.

9

Procurement Management Plan

Defines how procurement decisions, vendors, and contracts will be managed.

PROCUREMENT MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 20, 2026

Procurement Integration

Area	Integration Approach
Scope	Procurements are integrated with the WBS work packages they support. SOW scope must trace to WBS and Requirements Documentation.
Schedule	Procurement milestones (RFQ release, award, deliverable acceptance) are integrated into the project schedule and tracked weekly by the PM.
Documentation	All RFQs, evaluation results, signed SOWs, vendor deliverables, and acceptance records stored in the project SharePoint under /Procurement.
Risk	Procurement risks (vendor capacity, deliverable quality, payment terms) tracked in the Risk Register. Lead-time risks reflected in schedule contingency.
Reporting	Procurement status reported in the weekly project status report: open RFQs, awarded contracts, deliverable status, payment status.

Timing of Key Procurement Activities

Date	Activity
May 22, 2026	Issue RFQ for Frontend Contractor (3 vendors)
Jun 12, 2026	Receive vendor proposals; evaluation begins
Jun 26, 2026	Award Frontend Contractor SOW
Jun 30, 2026	Issue RFQ for WCAG 2.1 AA Audit (3 vendors)
Jul 24, 2026	Award WCAG Audit SOW
Jul 1, 2026	Renew CMS license (existing supplier; 12-month term)
Aug 15, 2026	Stock imagery purchase order issued
Sep 21, 2026	Frontend Contractor mid-engagement checkpoint
Oct 30, 2026	All vendor deliverables accepted
Dec 15, 2026	Final vendor invoices reconciled and paid

Performance Metrics

Item	Metric	Measurement Method
On-time delivery	% of vendor milestones met on or before agreed date	Track per milestone; ≥ 90% target
Quality	% of vendor deliverables accepted on first review	Track per deliverable; ≥ 80% target
Cost adherence	Variance between agreed price and final invoice	Track per contract; ≤ 5% variance target

PROCUREMENT MANAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 20, 2026

Roles, Responsibility, and Authority

Role	Responsibility	Authority
Project Manager (Andrew)	Initiate procurements; manage RFQ process; sign SOWs ≤ $5,000; manage vendor performance.	Sign contracts up to $5,000; approve vendor deliverables; release contingency.
Sponsor (Mary)	Authorize procurements > $5,000; final escalation.	Sign contracts > $5,000; approve management reserve.
Procurement Department	Run formal RFQ process; legal review of SOWs; vendor qualification.	Veto over non-approved suppliers; require Legal review on contracts > $25,000.
Bob (Tech Lead)	Author technical SOWs; technical review of vendor deliverables.	Approve / reject vendor technical deliverables.

Assumptions and Constraints

Category	Assumption / Constraint
Assumption	Vendors on the firm's approved supplier list are available within 2 weeks of SOW signing.
Assumption	Standard firm Net 30 payment terms accepted by all vendors.
Constraint	All vendor selections must come from the firm's approved supplier list unless waived by Procurement.
Constraint	Contracts > $25,000 require Legal and Procurement review (does not apply to this project — all contracts < $25K).
Constraint	All payments in USD; foreign-currency vendors out of scope.

Legal Jurisdiction and Currency

All contracts governed by U.S. (state of New York) law. All amounts in U.S. dollars (USD). Disputes resolved first via good-faith negotiation; if unresolved, mediation in New York County before any litigation.

Independent Estimates

For procurements > $5,000, the PM produces an independent cost estimate before issuing the RFQ. Independent estimate for the Frontend Contractor SOW is $2,400 – $3,200; for the WCAG audit, $3,500 – $5,000. These estimates are kept confidential during evaluation.

Risk Management

Procurement-related risks tracked in the Risk Register (see R-03 contractor unavailability; R-07 vendor outage at cutover). Mitigations include pre-qualified backup suppliers, fixed-price contracts to limit cost risk, and milestone-based payments to limit performance risk.

Prequalified Sellers

1. **WebCraft Studios** – Frontend / React / accessibility specialist (selected for Frontend SOW)
2. **AccessibleWeb Inc.** – WCAG 2.1 AA audit specialist (selected for audit SOW)
3. **BrightDigital Agency** – Backup frontend contractor
4. **InclusiveLabs** – Backup WCAG audit vendor

10

Stakeholder Management Plan

Defines strategies for engaging stakeholders effectively throughout the project.

STAKEHOLDER ENGAGEMENT PLAN

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 16, 2026

Stakeholder	Unaware	Resistant	Neutral	Supportive	Leading
Mary (CEO / Sponsor)					CD
Andrew (Project Manager)					CD
Bob (Web Developer)				C	D
Bill (UX / Designer)				C	D
Christine (Content)				CD	
Marketing Lead				C	D
Sales Lead			C	D	
Consultant Community (500+)			C	D	
Fortune 500 Prospects	C		D		
IT / Hosting Operations			C	D	
Legal / Compliance			C	D	
Hosting / CMS Vendor			C	D	

***C** = Current level of engagement* ***D** = Desired level of engagement* ***CD** = current matches desired*

Pending Stakeholder Changes	Stakeholder Relationships
• **Bob, Bill, Marketing Lead:** Move from Supportive to Leading during the build phase as decision authority is delegated. • **Sales Lead, Consultant Community:** Move from Neutral to Supportive ahead of content collection and launch. • **IT/Hosting Operations, Legal/Compliance:** Move from Neutral to Supportive by engaging at architecture review and design phase respectively. • **Fortune 500 Prospects:** Move from Unaware to Neutral at launch via press and outbound campaigns.	• Mary (Sponsor) → close ties to Marketing Lead and CFO; ultimate authority on brand decisions. • Marketing Lead and Sales Lead are peers in the commercial organization — alignment between them matters for handoff at launch. • IT/Hosting Operations is the post-launch owner — relationship managed jointly by PM and Bob. • Consultant Community (500+) is influenced by regional leadership; firm-wide messaging from Mary is the most effective reach. • Hosting/CMS Vendor relationship managed via Procurement; single point of contact is Bob.

STAKEHOLDER ENGAGEMENT PLAN – APPROACH

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 16, 2026

Stakeholder	C → D	Approach	Information Needs	Frequency & Method
Mary (CEO / Sponsor)	**L → L**	Already leading; sustain through weekly 1:1s with PM, monthly steering reviews, and personal sign-off on brand decisions.	High-level status, brand decisions, budget variance, F500 buyer feedback.	**Freq:** Weekly status; monthly steering **Method:** Email summary + 30-min meeting **Style:** Push (concise) + Interactive for decisions
Andrew (Project Manager)	**L → L**	Drives engagement of all other stakeholders; uses this matrix as a personal management tool, updated monthly.	Full project performance data; all logs and registers.	**Freq:** Continuous **Method:** All channels **Style:** Owns communications
Bob (Web Developer)	**S → L**	Move to Leading by giving Bob technical decision authority on stack/architecture and inviting him to sponsor design reviews for cross-team visibility.	Requirements, design specs, dependency schedule, defect priorities.	**Freq:** Daily during build; weekly otherwise **Method:** Daily standup + ticket system **Style:** Interactive (working sessions)
Bill (UX / Designer)	**S → L**	Move to Leading by partnering Bill directly with the Sponsor on brand reviews — owning the relationship rather than going through the PM.	Brand guidelines, sponsor feedback, accessibility requirements.	**Freq:** Daily during design; weekly otherwise **Method:** Working sessions + design review meetings **Style:** Interactive
Christine (Content)	**S → S**	Already supportive; sustain by ensuring consultant SMEs respond to her content requests on time. PM to escalate consultant unresponsiveness.	Brand voice guide, content templates, consultant SME availability.	**Freq:** Weekly during content production **Method:** Editorial planning meetings + email **Style:** Interactive + Pull (shared content board)
Marketing Lead	**S → L**	Move to Leading by giving the Marketing Lead joint ownership of post-launch operations and analytics dashboard design early.	Launch plan, lead-flow metrics, content workflow, training schedule.	**Freq:** Weekly through launch; monthly post-launch **Method:** Steering meeting + dashboard **Style:** Push + Interactive
Sales Lead	**N → S**	Move to Supportive by demonstrating CRM lead-routing improvements early; involve Sales in defining lead-quality metrics.	Lead-form fields, CRM integration specs, expected MQL volume.	**Freq:** Bi-weekly; daily during launch week **Method:** Working sessions + CRM demo **Style:** Interactive
Consultant Community (500+)	**N → S**	Move to Supportive via firm-wide kickoff communication from Mary, easy bio submission tools, and recognition of consultants featured in case studies.	Why this matters; how to submit bio; deadlines.	**Freq:** Major milestones only (kickoff, content due, launch) **Method:** Firm-wide email + intranet posts **Style:** Push (broadcast) + Pull (intranet)

Stakeholder	C → D	Approach	Information Needs	Frequency & Method
Fortune 500 Prospects	**U → N**	Move from Unaware to Neutral via a launch press release, LinkedIn campaign, and outreach by Sales using the new site as a talking point.	Service capabilities, case studies, thought leadership, contact path.	**Freq:** Launch + ongoing marketing **Method:** Pull (website) + outbound by Sales/Marketing **Style:** Pull
IT / Hosting Operations	**N → S**	Move to Supportive by involving IT Ops early in architecture review and giving them sign-off on hosting / monitoring / backup design before build.	Architecture, security review, runbook draft, monitoring requirements.	**Freq:** Monthly during planning/build; daily at cutover **Method:** Architecture review + handoff meeting **Style:** Interactive + Push (handoff docs)
Legal / Compliance	**N → S**	Move to Supportive by engaging Legal early on privacy/GDPR design and accessibility requirements — not at the end.	Privacy policy, cookie consent design, accessibility audit findings, vendor contracts.	**Freq:** At each phase gate **Method:** Document review + sign-off meetings **Style:** Push (drafts) + Interactive (review)
Hosting / CMS Vendor	**N → S**	Sustain Supportive engagement via clear SOW, single point of contact (Bob), and weekly check-ins during build phase.	SOW, deliverable acceptance criteria, payment schedule.	**Freq:** Weekly during build; on-demand after launch **Method:** Account manager calls + ticket system **Style:** Push + Interactive

11

Change Management Plan

Defines how changes to the project baselines will be requested and controlled.

CHANGE MANAGEMENT PLAN

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date Prepared: May 7, 2026

Purpose

This Change Management Plan defines how changes to the project scope, schedule, cost, quality, resources, or other baselines will be requested, evaluated, approved, implemented, and closed for the Mary's Consulting – New Company Website project.

Change Control Approach

All requested changes will be submitted via a Change Request form and logged in the Change Log by the Project Manager (Andrew). Changes are evaluated for impact on scope, schedule, cost, quality, and risk before being routed for approval. The project follows an Integrated Change Control process aligned with PMBOK Guide 8th Edition.

Change Control Board (CCB)

The CCB consists of:
- Mary (Sponsor / CEO) – Chair, final approval authority
- Andrew (Project Manager) – Coordinator, impact analysis owner
- Marketing Lead – Brand and content authority
- IT/Infrastructure Lead – Technical and security authority

The CCB meets weekly during execution; emergency reviews may be called within 24 hours.

Change Request Process

1. Submit – Any stakeholder may submit a Change Request to the PM.
2. Log – PM logs the request in the Change Log within 1 business day.
3. Analyze – PM and SMEs assess scope, cost, schedule, quality, and risk impact.
4. Decide – CCB reviews and approves, defers, or rejects the request.
5. Implement – Approved changes are incorporated into baselines and communicated.
6. Verify and Close – Implementation is verified and the request is closed in the log.

Approval Authority Thresholds

• ≤ $1,000 and ≤ 2 days: PM may approve and inform CCB.
• $1,001 – $5,000 or 3–5 days: CCB approval required.
• > $5,000, > 5 days, or change to Go-Live milestone: Sponsor (Mary) approval required.
• Any change affecting brand, security, or legal: relevant SME approval required in addition to CCB.

Documentation and Communication

All change requests, decisions, and rationale are recorded in the Change Log and Change Request forms. Approved changes are communicated to the team via the weekly status meeting and the project Slack channel within 2 business days of approval.

Tools and Templates

Change Request form, Change Log, Change Request Assessment, Change Request Approved – all maintained in the project SharePoint site. Configuration items are tracked under the Configuration Management Plan.

12

Configuration Management Plan

Defines how project artifacts will be identified, versioned, and audited.

CONFIGURATION MANAGEMENT PLAN

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date Prepared: May 7, 2026

Purpose

This Configuration Management Plan establishes how project artifacts and product components for the Mary's Consulting – New Company Website will be identified, controlled, versioned, and audited throughout the project lifecycle.

Configuration Items (CIs)

The following items are placed under configuration control:
- All project management plan components and baselines
- Project charter, scope statement, WBS, WBS dictionary
- Requirements documentation and traceability matrix
- Website source code, CMS templates, and CI/CD pipeline configuration
- Visual design assets, brand guidelines, content files
- Environment configuration (Dev / Staging / Prod)
- Vendor agreements and statements of work

Identification and Naming

Each CI is assigned a unique identifier in the format MC-WEB-[CATEGORY]-[NNNN]-vX.Y (for example, MC-WEB-DOC-0012-v1.3). Categories include DOC (documents), CODE, DESIGN, CONFIG, and CONTRACT.

Version Control

• Documents: stored in SharePoint with built-in versioning; major versions for approved baselines, minor versions for working drafts.
• Code: Git repository (main, develop, feature branches); semantic versioning for releases.
• Design assets: Figma version history with named milestones.
• All baselined items are locked; changes require an approved Change Request.

Change Control Linkage

Configuration changes follow the process defined in the Change Management Plan. Approved changes update the relevant CI version and are reflected in the Change Log.

Configuration Status Accounting

The PM (Andrew) maintains a Configuration Item Register listing each CI, current version, owner, status, and last-changed date. Status is reported in the weekly Project Status Report.

Configuration Audits

• Functional audit at end of Test phase: verify product matches requirements.
• Physical audit at Go-Live: verify all CIs (code, content, configs) deployed match approved versions.
• Audit results are logged and any discrepancies handled via change requests.

Roles and Responsibilities

• PM (Andrew): owns the configuration management process, approves CI register changes.
• Developers (Bob, Bill): maintain code and config CIs.
• Designer / Content Lead (Christine): maintains design and content CIs.
• Sponsor (Mary): approves baseline configurations at phase gates.

13

Scope Baseline

The approved Project Scope Statement, WBS, and WBS Dictionary.

PROJECT SCOPE STATEMENT

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 9, 2026

Project Scope Description

Design, develop, and launch a new public-facing marketing website for Mary's Consulting at marysconsulting.com. The site will replace the current legacy site and serve as the firm's primary digital storefront for Fortune 500 buyers. It will include an updated brand identity, a service catalog covering project management consulting, a consultant directory of 500+ global consultants, a case-study library, a thought-leadership blog, and a Contact / Request-for-Proposal lead-capture flow integrated with the company CRM. The site will be responsive (desktop, tablet, mobile), WCAG 2.1 AA accessible, GDPR compliant, and managed via a CMS that allows non-technical staff to publish content without engineering involvement.

Project Deliverables

1. **Approved brand and visual design system** – brand guidelines, color palette, typography, component library.
2. **Information architecture and wireframes** – sitemap, page templates, interaction flows.
3. **Content set** – home, services, case studies (≥ 20), consultant directory entries, blog seed content (≥ 10 posts), legal pages.
4. **CMS-driven website** – fully developed responsive site with editor workflow.
5. **CRM integration** – contact and RFP forms routed to the company CRM via API with logging and retry.
6. **Hosting environment** – production hosting, DNS, SSL, CDN, monitoring, and backup.
7. **Test & QA artifacts** – test plan, executed test cases, performance report, third-party WCAG 2.1 AA audit report.
8. **Production launch** – Go-Live event, post-launch support transition.
9. **Project management documents** – charter, plans, logs, status reports, lessons learned, formal acceptance.

Product Acceptance Criteria

- All Must-priority requirements verified and validated as documented in the Requirements Traceability Matrix.
- 75th-percentile Largest Contentful Paint (LCP) < 2.5 seconds in the pre-launch performance test.
- Third-party WCAG 2.1 AA audit returns zero Severity-1 findings.
- User Acceptance Testing completed with no open Severity-1 or Severity-2 defects.
- CEO (Mary) signs off on brand/visual fit.
- Marketing Lead signs off on content and CMS workflow.
- Legal/Compliance signs off on GDPR and accessibility.
- Production hosting documented and handed off to IT/Hosting Operations.

Project Exclusions

The following items are explicitly **OUT OF SCOPE** for this project:

- Internal consultant portal (extranet, time tracking, client workspaces).
- Client project delivery tools, dashboards, or collaboration spaces.
- Billing, invoicing, or financial-system integration.
- Paid advertising campaigns, SEO content production beyond launch seed, and ongoing marketing operations.
- Multi-language translation of consultant bios at launch (deferred to a future phase).
- Mobile native applications (iOS / Android).
- Migration of historical blog content older than 24 months.

PROJECT SCOPE STATEMENT

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 9, 2026

Project Constraints


Budget: Total project cost capped at $150,000 USD. Any expenditure beyond this requires sponsor approval.
Schedule: Production launch must occur on or before the November 2026 Go-Live milestone.
Resources: Core team is fixed at the Project Manager (Andrew) plus three team members (Bob, Bill, Christine). Functional manager approval is required to add resources.
Brand approval: Final brand and visual direction must be approved personally by the CEO (Mary). No delegation of this approval is permitted.
Quality: Site must meet WCAG 2.1 AA, GDPR, and the firm's IT security standards. These are non-negotiable.
Technology: CMS selection must be from the firm's approved technology list; hosting must use the firm's approved cloud provider.
PM Authority: The PM may approve expenditures up to $5,000 per item and reallocate up to 10% within budget categories. Anything beyond requires sponsor approval.

Project Assumptions

- The three core team members will be available at planned allocations through project close.
- Mary will be available for design reviews at agreed checkpoints; turnaround on brand decisions ≤ 5 business days.
- The existing CRM offers a supported integration method (API or vendor connector) for lead capture.
- Consultants worldwide will provide updated bios and case-study content within agreed deadlines.
- WCAG 2.1 AA is the accepted accessibility standard for the project.
- Marketing will execute SEO and content campaigns post-launch to drive traffic; the project itself does not include those activities.
- The hosting/CMS vendor's standard SLA (≥ 99.5% uptime) is acceptable to IT Operations.
- No major change in the firm's service offerings during the project timeline.

WORK BREAKDOWN STRUCTURE

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 10, 2026

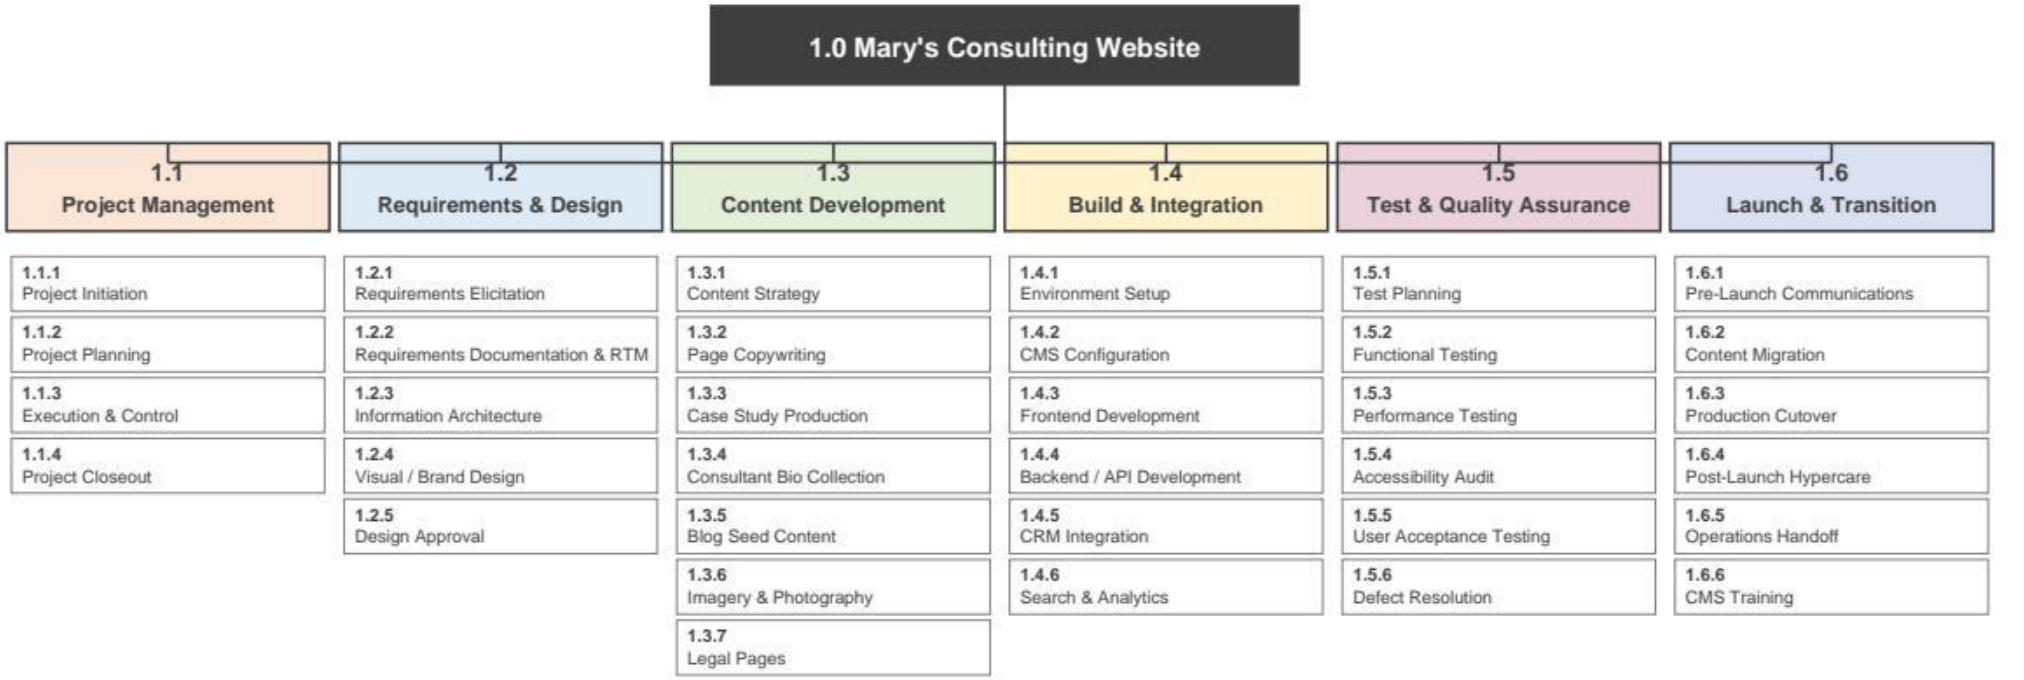

WORK BREAKDOWN STRUCTURE – NUMBERED LIST

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 10, 2026

1.1 Project Management

- 1.1.1 Project Initiation
- 1.1.2 Project Planning
- 1.1.3 Execution & Control
- 1.1.4 Project Closeout

1.2 Requirements & Design

- 1.2.1 Requirements Elicitation
- 1.2.2 Requirements Documentation & RTM
- 1.2.3 Information Architecture
- 1.2.4 Visual / Brand Design
- 1.2.5 Design Approval

1.3 Content Development

- 1.3.1 Content Strategy
- 1.3.2 Page Copywriting
- 1.3.3 Case Study Production
- 1.3.4 Consultant Bio Collection
- 1.3.5 Blog Seed Content
- 1.3.6 Imagery & Photography
- 1.3.7 Legal Pages

1.4 Build & Integration

- 1.4.1 Environment Setup
- 1.4.2 CMS Configuration
- 1.4.3 Frontend Development
- 1.4.4 Backend / API Development
- 1.4.5 CRM Integration
- 1.4.6 Search & Analytics

1.5 Test & Quality Assurance

- 1.5.1 Test Planning
- 1.5.2 Functional Testing
- 1.5.3 Performance Testing
- 1.5.4 Accessibility Audit
- 1.5.5 User Acceptance Testing
- 1.5.6 Defect Resolution

1.6 Launch & Transition

- 1.6.1 Pre-Launch Communications
- 1.6.2 Content Migration
- 1.6.3 Production Cutover
- 1.6.4 Post-Launch Hypercare
- 1.6.5 Operations Handoff
- 1.6.6 CMS Training

WBS DICTIONARY – SUMMARY

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 10, 2026

Summary table of all work packages. Detailed entries for representative work packages follow.

Code	Work Package	Owner	Effort	Key Deliverable	Acceptance Criteria
1.1 Project Management					
1.1.1	Project Initiation	Andrew (PM)	40 hrs	Approved Project Charter; Stakeholder Register; Assumption Log	Charter signed by Mary (Sponsor); register & log baselined.
1.1.2	Project Planning	Andrew (PM)	80 hrs	Subsidiary management plans; Scope, Schedule, Cost baselines; Risk Register	PM Plan approved by Sponsor; baselines locked.
1.1.3	Execution & Control	Andrew (PM)	200 hrs	Weekly status reports; Change Log; Issue Log; updated Risk Register	Reports delivered weekly through Go-Live; no open Sev-1 issues at launch.
1.1.4	Project Closeout	Andrew (PM)	40 hrs	Lessons Learned; Formal Acceptance form; archived project records	Sponsor signs Formal Acceptance; lessons filed in OPA.
1.2 Requirements & Design					
1.2.1	Requirements Elicitation	Andrew (PM)	60 hrs	Interview notes; focus group output; questionnaire responses	≥ 90% of identified stakeholders consulted; raw data archived.
1.2.2	Requirements Documentation & RTM	Andrew (PM)	40 hrs	Requirements Documentation; Requirements Traceability Matrix	All Must/Should reqs have acceptance criteria and verification method.
1.2.3	Information Architecture	Bill (UX)	50 hrs	Sitemap; user flows; wireframes for top 10 templates	Sponsor and Marketing Lead sign off on IA.
1.2.4	Visual / Brand Design	Bill (UX)	120 hrs	Brand system; high-fidelity mockups; component library	Mary (CEO) personally signs off on brand fit.
1.2.5	Design Approval	Andrew (PM)	16 hrs	Approved design package; signed approval record	Sponsor signature on final design package.
1.3 Content Development					
1.3.1	Content Strategy	Christine	30 hrs	Content strategy doc; voice and tone guide; editorial calendar	Marketing Lead approves strategy.
1.3.2	Page Copywriting	Christine	100 hrs	Final copy for ~25 marketing pages (home, services, about, contact)	Marketing Lead and Legal review and approve all copy.
1.3.3	Case Study Production	Christine	80 hrs	≥ 20 case studies with consistent format	Each case study client-cleared (anonymized where required).
1.3.4	Consultant Bio Collection	Christine	60 hrs	Bios for ≥ 500 consultants in directory format	≥ 95% of active consultants represented; bios edited for consistency.
1.3.5	Blog Seed Content	Christine	40 hrs	≥ 10 thought-leadership articles ready to publish	Marketing Lead approves; SEO keywords mapped.
1.3.6	Imagery & Photography	Bill (UX)	40 hrs	Licensed image library; consultant headshots where available	All images licensed; alt-text drafted for accessibility.
1.3.7	Legal Pages	Andrew (PM)	16 hrs	Privacy Policy, Cookie Policy, Terms of Use	Legal/Compliance sign-off on all three pages.
1.4 Build & Integration					
1.4.1	Environment Setup	Bob (Dev)	40 hrs	Dev, staging, and production environments; CI/CD pipeline	All three environments deployable; CI build passes.

Code	Work Package	Owner	Effort	Key Deliverable	Acceptance Criteria
1.4.2	CMS Configuration	Bob (Dev)	60 hrs	Configured CMS with content types, roles, and editor workflow	Marketing can author and publish a sample page end-to-end.
1.4.3	Frontend Development	Bob (Dev)	180 hrs	Built page templates and components per design system	Frontend matches approved designs across responsive breakpoints.
1.4.4	Backend / API Development	Bob (Dev)	120 hrs	Form handling; consultant directory search API; admin endpoints	All endpoints documented; integration tests pass.
1.4.5	CRM Integration	Bob (Dev)	60 hrs	Form-to-CRM connector with logging and retry; field mapping	100% of test submissions reach CRM in < 5 minutes.
1.4.6	Search & Analytics	Bob (Dev)	40 hrs	Site search; Google Analytics & tag manager configured; dashboards	Analytics dashboard validated by Marketing Lead.
1.5 Test & Quality Assurance					
1.5.1	Test Planning	Andrew (PM)	20 hrs	Test plan; test cases mapped to requirements via RTM	Test plan reviewed by team; coverage ≥ 95% of Must/Should requirements.
1.5.2	Functional Testing	Bob (Dev)	60 hrs	Test execution log; defect list	100% of Must-priority test cases executed; no open Sev-1 defects.
1.5.3	Performance Testing	Bob (Dev)	30 hrs	Performance test report (Lighthouse / WebPageTest)	75th-percentile LCP < 2.5s on top 10 pages.
1.5.4	Accessibility Audit	Bill (UX)	40 hrs	Third-party WCAG 2.1 AA audit report	Zero Severity-1 accessibility findings.
1.5.5	User Acceptance Testing	Andrew (PM)	40 hrs	UAT execution log; sign-off forms	Sponsor and Marketing Lead sign off; no Sev-1 or Sev-2 defects open.
1.5.6	Defect Resolution	Bob (Dev)	60 hrs	Closed defects; regression test results	All Sev-1 / Sev-2 defects closed and re-tested before launch.
1.6 Launch & Transition					
1.6.1	Pre-Launch Communications	Christine	16 hrs	Internal announcement; external press and social assets	Marketing Lead approves communications plan.
1.6.2	Content Migration	Christine	40 hrs	Migrated case studies and selected blog content from legacy site	100% of in-scope content migrated and QA-verified.
1.6.3	Production Cutover	Bob (Dev)	24 hrs	DNS updated; SSL active; production deployment completed	Site live on marysconsulting.com with no downtime errors during cutover window.
1.6.4	Post-Launch Hypercare	Bob (Dev)	60 hrs	2-week active monitoring; rapid-response fixes	All Sev-1 issues resolved in < 4 hours during hypercare.
1.6.5	Operations Handoff	Andrew (PM)	20 hrs	Runbooks; monitoring config; signed handoff document	IT/Hosting Operations signs handoff form.
1.6.6	CMS Training	Christine	16 hrs	4-hour training session held; quick-reference guide	Marketing team can independently publish a page after training.

Summary continues on detailed entries

WBS DICTIONARY – ENTRY 1 OF 3

Work Package Name:	Project Planning	**Code of Account:**	1.1.2

Description of Work:	Develop the integrated Project Management Plan, subsidiary management plans, and the Scope, Schedule, and Cost baselines for the website project.
Responsible Party:	Andrew (PM)
Assumptions & Constraints:	Sponsor turnaround on plan review ≤ 5 business days.

Milestones & Due Dates

#	Milestone	Due Date
1	Charter approved (input received)	May 5, 2026
2	Subsidiary plans drafted	May 25, 2026
3	Baselines approved by Sponsor	Jun 15, 2026

Resources & Cost Estimate

Activity / Resource	Hours / Units	Rate ($/hr)	Cost ($)
Project Manager	80	75	$6,000
Subject-matter expert (Marketing)	8	65	$520
Subject-matter expert (Legal)	4	90	$360
Total			**$6,880**

Quality Requirements:	PMI / PMBOK 8 alignment. All baselines subject to Integrated Change Control after approval.
Acceptance Criteria:	Sponsor (Mary) signs Project Management Plan; all subsidiary plans complete; baselines locked.
Technical Information:	MS Project for schedule; Excel for cost; company SharePoint for plan storage.
Agreement Information:	No external contracts at this stage.

WBS DICTIONARY – ENTRY 2 OF 3

Work Package Name:	Frontend Development	**Code of Account:**	1.4.3

Description of Work:	Build the website's user interface including all page templates and reusable components in line with the approved design system. Implement responsive behavior across desktop, tablet, and mobile breakpoints.
Responsible Party:	Bob (Web Developer / Tech Lead)
Assumptions & Constraints:	Design system finalized before this package starts; CMS environment available.

Milestones & Due Dates

#	Milestone	Due Date
1	Component library complete	Aug 10, 2026
2	All page templates built	Sep 5, 2026
3	Frontend handed to QA	Sep 15, 2026

Resources & Cost Estimate

Activity / Resource	Hours / Units	Rate ($/hr)	Cost ($)
Lead Developer (Bob)	120	95	$11,400
Frontend contractor	60	80	$4,800
Image / icon assets (license)	1	—	$1,200
Total			**$17,400**

Quality Requirements:	Code adheres to firm's frontend coding standards; passes ESLint & accessibility linter; ≥ 80% unit-test coverage on components.
Acceptance Criteria:	Frontend matches approved designs; responsive at 320px, 768px, 1280px; Lighthouse Performance ≥ 90 on top 10 pages.
Technical Information:	Stack: HeadlessCMS + React/Next.js + Tailwind (per firm's approved tech list). Hosted in approved cloud provider.
Agreement Information:	Contractor SOW for frontend support, $4,800 fixed.

WBS DICTIONARY – ENTRY 3 OF 3

Work Package Name:	Production Cutover	**Code of Account:**	1.6.3

Description of Work:	Execute the Go-Live cutover: deploy final build to production, update DNS to point marysconsulting.com to the new infrastructure, verify SSL, and validate site availability.
Responsible Party:	Bob (Web Developer / Tech Lead)
Assumptions & Constraints:	All UAT defects resolved before cutover; comms plan executed (stakeholders notified).

Milestones & Due Dates

#	Milestone	Due Date
1	Cutover plan approved	Oct 25, 2026
2	DNS updated	Nov 7, 2026
3	Go-Live confirmed	Nov 7, 2026

Resources & Cost Estimate

Activity / Resource	Hours / Units	Rate ($/hr)	Cost ($)
Lead Developer (Bob)	16	95	$1,520
IT / Hosting Operations support	8	110	$880
Total			**$2,400**

Quality Requirements:	Zero-error cutover window; HTTPS enforced; Core Web Vitals within target on top 10 pages immediately after cutover.
Acceptance Criteria:	Site live on marysconsulting.com; SSL validated; smoke tests pass; rollback plan validated and documented.
Technical Information:	DNS managed via firm's registrar; cutover runbook in SharePoint.
Agreement Information:	Hosting vendor SLA in effect from cutover.

14

Schedule Baseline

The approved version of the schedule model used for measurement and control.

SCHEDULE BASELINE

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

Purpose

This document constitutes the approved **Schedule Baseline** for the Mary's Consulting Website project. Per PMBOK 8th edition, the schedule baseline is the approved version of the schedule model that can be changed only through formal change-control procedures. It is used as a basis for measuring schedule performance throughout the project.

Schedule Baseline Components

The Schedule Baseline consists of:

1. **Activity List** – defined activities derived from the WBS work packages.
2. **Activity Attributes** – detailed attributes for each activity.
3. **Duration Estimates** – approved duration for each activity.
4. **Milestone List** – key project milestones with target dates.
5. **Project Schedule Network Diagram** – sequenced activities with dependencies.
6. **Project Schedule** – calendar-based schedule with start and finish dates.
7. **Project Calendar** – working/non-working days governing the schedule.

Baseline Key Dates

Milestone	Date
Project Start (Charter approved)	May 08, 2026
Planning Complete; Baselines Locked	Jun 08, 2026
Requirements Approved	Jul 02, 2026
Design Approved	Aug 07, 2026
Build Complete	Oct 09, 2026
UAT Sign-off	Nov 19, 2026
Production Go-Live	Nov 24, 2026
Hypercare Complete	Dec 10, 2026
Operations Handoff	Dec 15, 2026
Project Closeout	Dec 29, 2026

Baseline Approval

Project Manager	Sponsor
_____	_____
Andrew	Mary (CEO)
Date: Jun 08, 2026	Date: Jun 08, 2026

15


Cost Baseline

The approved time-phased budget used to measure and control project costs.

COST BASELINE

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 15, 2026

Time-phased cumulative cost (S-curve) and monthly spend distribution. The cost baseline is direct cost plus contingency reserve. Management reserve sits outside the cost baseline.

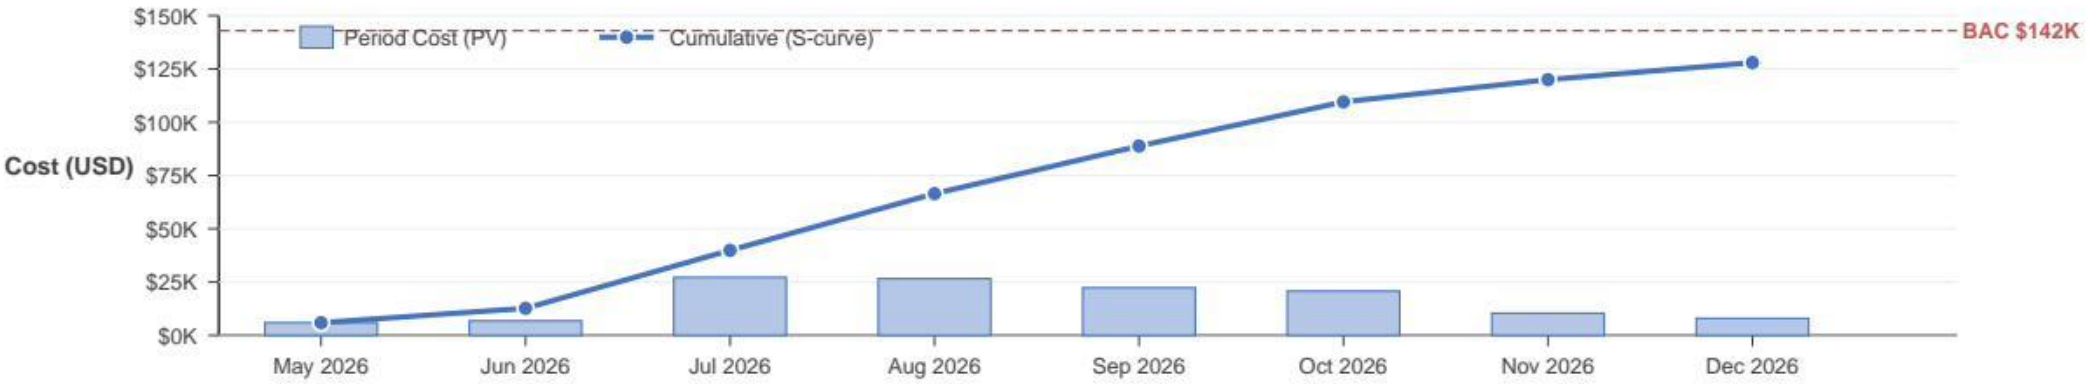

Period	Period Cost (PV)	Cumulative (BAC partial)	% of Direct
May 2026	$5,915	$5,915	4.6%
Jun 2026	$6,775	$12,690	9.9%
Jul 2026	$27,201	$39,891	31.2%
Aug 2026	$26,589	$66,480	52.0%
Sep 2026	$22,327	$88,807	69.4%
Oct 2026	$20,733	$109,540	85.6%
Nov 2026	$10,416	$119,956	93.8%
Dec 2026	$7,996	$127,952	100.0%
Direct Cost Total	**$127,952**	**$127,952**	**100.0%**
+ Contingency Reserve			**$15,000**
= Cost Baseline (BAC)			**$142,952**
+ Management Reserve (sponsor-held)			**$7,500**
= Total Funding Required			**$150,452**

16

Performance Measurement Baseline

Integrated scope, schedule, and cost baseline used for Earned Value Management.

PERFORMANCE MEASUREMENT BASELINE (PMB)

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

The Performance Measurement Baseline (PMB) is the integrated scope, schedule, and cost baseline used to measure and manage project performance via Earned Value Management (EVM). The PMB consists of the approved Scope Baseline (Project Scope Statement, WBS, WBS Dictionary), Schedule Baseline (Project Schedule), and Cost Baseline (time-phased budget). Performance is reported monthly using CV, SV, CPI, SPI, EAC, and VAC. Variance thresholds: ±10% triggers analysis; ±15% triggers a corrective-action plan and Change Request.

WBS	Phase / Work Package	Scope Deliverable	Planned Duration	Budget (PV)
1.0	Project Management	Plans, reports, governance	30 weeks	$22,000
2.0	Requirements & Design	Requirements doc, IA, wireframes, visual design	6 weeks	$28,000
3.0	Content Development	Page copy, images, video, SEO content	8 weeks	$24,000
4.0	Build & Integration	CMS build, CRM integration, dev/staging envs	10 weeks	$45,000
5.0	Test & QA	Functional, performance, security, UAT	4 weeks	$15,000
6.0	Launch & Transition	Production deploy, training, hypercare	3 weeks	$10,000
—	Management Reserve	Sponsor-controlled reserve for unknown-unknowns	n/a	$10,000
	TOTAL PMB (BAC)		30 weeks	$154,000

17

Project Life Cycle Description

Description of the phases the project will pass through from start to finish.

PROJECT LIFE CYCLE DESCRIPTION

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date Prepared: May 7, 2026

Overview

The Mary's Consulting – New Company Website project follows a hybrid life cycle: a predictive (plan-driven) approach for governance, scope baselining, and procurement; and an adaptive (iterative) approach for design, content, and build phases. The project is divided into six sequential phases with internal iterations inside the Design and Build phases.

Phase 1 – Initiation (Weeks 1–2)

Charter approved, sponsor commitment confirmed, PM and core team assigned, high-level stakeholder register established. Phase gate: Charter sign-off.

Phase 2 – Planning (Weeks 3–6)

Full PM Plan and subsidiary plans developed and baselined. Requirements gathered, WBS decomposed, schedule and cost baselines set, risks identified. Phase gate: PM Plan approval by sponsor.

Phase 3 – Design (Weeks 7–12)

Iterative wireframes, visual design, and prototype reviews with stakeholders. Two-week sprint cadence with sponsor demos. Phase gate: Design approval and content scope freeze.

Phase 4 – Build & Integration (Weeks 13–22)

Iterative CMS development, CRM integration, content loading, and unit testing. Two-week sprints; demo every sprint; deployable build at end of each sprint. Phase gate: Code-complete, ready for system test.

Phase 5 – Test & QA (Weeks 23–26)

Functional, performance, security, accessibility, and User Acceptance Testing. Defect triage and remediation. Phase gate: UAT sign-off.

Phase 6 – Launch & Closeout (Weeks 27–30)

Production deployment, DNS cut-over, stakeholder training, two-week hypercare, lessons learned, formal acceptance, and project closeout. Phase gate: Formal Acceptance and Project Closeout signed by sponsor.

Phase Gate Review Process

Each phase ends with a formal phase-gate review attended by the PM, sponsor, and key stakeholders. Outcomes: Proceed, Proceed with conditions, Hold, or Cancel. Decisions are documented in the Decision Log.

18

Development Approach

Method used to create and evolve the product, service, or result.

DEVELOPMENT APPROACH

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date Prepared: May 7, 2026

Approach Selection

A hybrid development approach has been selected for the Mary's Consulting – New Company Website project. Predictive planning provides governance and budget discipline expected by the sponsor; adaptive iterations within Design and Build phases manage uncertainty in look-and-feel, content, and integration with the existing CRM.

Rationale

• Requirements for governance, security, and brand are well-defined and stable → predictive.
• Visual design, UX, and content require frequent stakeholder feedback → adaptive.
• Fortune-500 clients expect predictable delivery dates and a fixed Go-Live → predictive milestones.
• Integration risk with CRM is moderate; iterative spikes reduce risk earlier.

Cadence and Ceremonies

• Sprint length: 2 weeks during Design and Build phases.
• Sprint planning: Monday morning, 90 minutes.
• Daily stand-up: 15 minutes, 9:30 AM ET.
• Sprint review / demo: every other Friday with sponsor and key stakeholders.
• Sprint retrospective: every other Friday after demo, 60 minutes.
• Phase-gate review: end of each major phase.

Definition of Ready (DoR)

A backlog item is Ready when it has: a clear user story or requirement, acceptance criteria, design references (if applicable), estimated effort, and no blocking dependencies.

Definition of Done (DoD)

A backlog item is Done when it: meets acceptance criteria, has passed peer code review, has automated tests where applicable, has been deployed to the staging environment, has been verified by the PM or designated reviewer, and is documented.

Tooling

• Backlog and sprint management: Jira.
• Source control: GitHub (private repo).
• CI/CD: GitHub Actions deploying to AWS staging and production.
• Design: Figma.
• Communication: Slack channel #mc-website; weekly status to all stakeholders via email.

Quality and Release Strategy

Continuous integration on every commit; deployment to staging on merge to develop; production deployments only at scheduled releases approved by the PM. A single Go-Live release marks

public launch; subsequent enhancements are out of scope and handled via post-project work intake.
