PROJECT DOCUMENTS

Project Documents

33 Supporting Project Documents

Project Title:	Mary's Consulting – New Company Website
Project Manager:	Andrew (Project Manager)
Project Sponsor:	Mary (CEO)
Date Prepared:	May 7, 2026
Document Status:	Approved – Baselined
Version:	1.0

CONFIDENTIAL – Internal Use Only | Mary's Consulting © 2026

Project Documents – Contents

#	Section	Page
1	Activity Attributes	4
2	Activity List	10
3	Assumption Log	13
4	Basis of Estimates	15
5	Change Log	20
6	Cost Estimates	22
7	Cost Forecast	25
8	Duration Estimates	27
9	Issue Log	29
10	Lessons Learned Register	31
11	Milestone List	34
12	Physical Resources Assignments	36
13	Project Calendars	38
14	Project Communications	41
15	Project Schedule	43
16	Project Schedule Network Diagram	45
17	Project Scope Statement	48
18	Project Team Assignments	51
19	Quality Control Measurements	53
20	Quality Metrics	55
21	Quality Report	57
22	Requirements Documentation	59
23	Requirements Traceability Matrix	62

24	Resource Breakdown Structure	66
25	Resource Calendars	68
26	Resource Requirements	70
27	Risk Register	73
28	Risk Report	77
29	Schedule Data	80
30	Schedule Forecast	82
31	Stakeholder Register	84
32	Team Charter	87
33	Test and Evaluation Documents	90

1

Activity Attributes

Detailed attributes of each schedule activity (predecessors, resources, constraints).

ACTIVITY ATTRIBUTES – SUMMARY

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

Summary table for all activities. Detailed attribute entries follow for representative activities.

ID	Activity	WBS	Owner	Effort (hrs)	Duration (days)	Predecessors	Critical?
A001	Develop Project Charter	1.1.1	Andrew (PM)	20	5	—	Yes
A002	Identify Stakeholders	1.1.1	Andrew (PM)	16	3	A001	Yes
A003	Develop Subsidiary Plans	1.1.2	Andrew (PM)	60	12	A002	Yes
A004	Establish Baselines	1.1.2	Andrew (PM)	20	5	A003	Yes
A005	Project Closeout	1.1.4	Andrew (PM)	40	8	A045	Yes
A006	Conduct Requirements Interviews	1.2.1	Andrew (PM)	30	5	A004	Yes
A007	Run Requirements Focus Groups	1.2.1	Andrew (PM)	16	3	A006	—
A008	Distribute Consultant Questionnaire	1.2.1	Christine	12	7	A006	Yes
A009	Document Requirements & RTM	1.2.2	Andrew (PM)	40	5	A007, A008	Yes
A010	Develop Information Architecture	1.2.3	Bill (UX)	50	7	A009	Yes
A011	Develop Visual / Brand Design	1.2.4	Bill (UX)	120	15	A010	Yes
A012	Sponsor Design Review & Approval	1.2.5	Mary (Sponsor)	8	3	A011	Yes
A013	Develop Content Strategy	1.3.1	Christine	30	4	A009	—
A014	Write Marketing Page Copy	1.3.2	Christine	100	18	A013	—
A015	Produce Case Studies	1.3.3	Christine	80	20	A013	—
A016	Collect Consultant Bios	1.3.4	Christine	60	25	A013	—
A017	Write Blog Seed Content	1.3.5	Christine	40	10	A013	—
A018	Source / License Imagery	1.3.6	Bill (UX)	40	8	A012	—
A019	Draft Legal Pages	1.3.7	Andrew (PM)	16	4	A013	—
A020	Marketing & Legal Content Review	1.3.2	Andrew (PM)	24	5	A014, A015, A016, A017, A018, A019	—
A021	Set Up Dev / Staging / Prod Environments	1.4.1	Bob (Dev)	40	5	A012	Yes
A022	Configure CMS	1.4.2	Bob (Dev)	60	7	A021	Yes
A023	Build Component Library	1.4.3	Bob (Dev)	80	12	A022	Yes
A024	Build Page Templates	1.4.3	Bob (Dev)	100	15	A023	Yes
A025	Develop Backend APIs	1.4.4	Bob (Dev)	120	12	A022	—
A026	Implement CRM Integration	1.4.5	Bob (Dev)	60	8	A025	—
A027	Configure Search & Analytics	1.4.6	Bob (Dev)	40	5	A024	Yes
A028	Develop Test Plan	1.5.1	Andrew (PM)	20	3	A009	—
A029	Execute Functional Tests	1.5.2	Bob (Dev)	60	8	A024, A026, A027, A028	Yes

ID	Activity	WBS	Owner	Effort (hrs)	Duration (days)	Predecessors	Critical?
A030	Execute Performance Tests	1.5.3	Bob (Dev)	30	4	A029	Yes
A031	Conduct Accessibility Audit	1.5.4	Bill (UX)	40	5	A024	—
A032	Resolve Defects	1.5.6	Bob (Dev)	60	8	A029, A030, A031	Yes
A033	Conduct UAT	1.5.5	Andrew (PM)	40	5	A032	Yes
A034	Final UAT Sign-off	1.5.5	Mary (Sponsor)	8	2	A033	Yes
A035	Develop Launch Communications Plan	1.6.1	Christine	16	3	A012	—
A036	Migrate Content from Legacy Site	1.6.2	Christine	40	5	A020, A024	—
A037	Pre-Launch Internal Communications	1.6.1	Christine	8	2	A034, A035	Yes
A038	Production Cutover (Go-Live)	1.6.3	Bob (Dev)	16	1	A036, A037	Yes
A039	Post-Launch Hypercare	1.6.4	Bob (Dev)	60	10	A038	Yes
A040	CMS Training for Marketing	1.6.6	Christine	16	1	A038	—
A045	Operations Handoff	1.6.5	Andrew (PM)	20	3	A039, A040	Yes

Summary continues with detailed entries

ACTIVITY ATTRIBUTES – ENTRY 1 OF 3

ID:	A009	Activity:	Document Requirements & RTM

Description of Work:	Compile Requirements Documentation and the RTM.

Predecessor	Relationship	Lead/Lag	Successor	Relationship	Lead/Lag
A007	FS	0	A010	FS	0
A008	FS	0	A013	FS	0
			A028	FS	0

Number & Type of Team Resources Required:	1 × Andrew (PM); effort 40 hours over 5 working days
Skill Requirements:	PM (planning, facilitation); domain SME for the activity's content area
Required Resources:	MS Project; collaboration tools (firm SharePoint); applicable templates
Type of Effort:	Discrete (deliverable-based)
Location of Performance:	Hybrid – primary at firm office; remote-friendly for individual contributor work
Imposed Dates / Constraints:	Earliest start: Jun 26, 2026; Latest finish: Jul 02, 2026; constrained by predecessors
Assumptions:	Resource availability per Resource Mgmt Plan; no scope changes during this activity

ACTIVITY ATTRIBUTES – ENTRY 2 OF 3

ID:	A024	Activity:	Build Page Templates

Description of Work:	Home, services, case study, directory, blog templates.

Predecessor	Relationship	Lead/Lag	Successor	Relationship	Lead/Lag
A023	FS	0	A027	FS	0
			A029	FS	0
			A031	FS	0
			A036	FS	0

Number & Type of Team Resources Required:	1 × Bob (Dev); effort 100 hours over 15 working days
Skill Requirements:	PM (planning, facilitation); domain SME for the activity's content area
Required Resources:	MS Project; collaboration tools (firm SharePoint); applicable templates
Type of Effort:	Discrete (deliverable-based)
Location of Performance:	Hybrid – primary at firm office; remote-friendly for individual contributor work
Imposed Dates / Constraints:	Earliest start: Sep 14, 2026; Latest finish: Oct 02, 2026; constrained by predecessors
Assumptions:	Resource availability per Resource Mgmt Plan; no scope changes during this activity

ACTIVITY ATTRIBUTES – ENTRY 3 OF 3

ID:	A038	Activity:	Production Cutover (Go-Live)

Description of Work:	DNS update, SSL validation, smoke tests on production.

Predecessor	Relationship	Lead/Lag	Successor	Relationship	Lead/Lag
A036	FS	0	A039	FS	0
A037	FS	0	A040	FS	0

Number & Type of Team Resources Required:	1 × Bob (Dev); effort 16 hours over 1 working days
Skill Requirements:	PM (planning, facilitation); domain SME for the activity's content area
Required Resources:	MS Project; collaboration tools (firm SharePoint); applicable templates
Type of Effort:	Discrete (deliverable-based)
Location of Performance:	Hybrid – primary at firm office; remote-friendly for individual contributor work
Imposed Dates / Constraints:	Earliest start: Nov 24, 2026; Latest finish: Nov 24, 2026; constrained by predecessors
Assumptions:	Resource availability per Resource Mgmt Plan; no scope changes during this activity

2 Activity List

Comprehensive list of all schedule activities required to complete the project.

ACTIVITY LIST

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

ID	Activity	Description of Work
A001	Develop Project Charter	Draft, review, and obtain sponsor signature on the charter.
A002	Identify Stakeholders	Build the stakeholder register and stakeholder analysis.
A003	Develop Subsidiary Plans	Author scope, schedule, cost, quality, resource, comms, risk, and procurement subsidiary plans.
A004	Establish Baselines	Approve scope, schedule, and cost baselines with the sponsor.
A005	Project Closeout	Lessons learned, formal acceptance, archival.
A006	Conduct Requirements Interviews	Interview Mary, Marketing Lead, Sales Lead, IT, and Legal.
A007	Run Requirements Focus Groups	Two facilitated focus groups with the project team.
A008	Distribute Consultant Questionnaire	Send to consultant sample; allow 1 week for responses.
A009	Document Requirements & RTM	Compile Requirements Documentation and the RTM.
A010	Develop Information Architecture	Sitemap, user flows, wireframes for top 10 templates.
A011	Develop Visual / Brand Design	Brand system; high-fidelity mockups; component library.
A012	Sponsor Design Review & Approval	Sponsor walks through design package and signs off.
A013	Develop Content Strategy	Voice and tone guide; editorial calendar.
A014	Write Marketing Page Copy	Final copy for ~25 marketing pages.
A015	Produce Case Studies	Develop ≥ 20 case studies with client clearance.
A016	Collect Consultant Bios	Outreach to 500+ consultants; format bios consistently.
A017	Write Blog Seed Content	Draft and edit ≥ 10 thought-leadership articles.
A018	Source / License Imagery	License stock imagery; collect consultant headshots; alt-text.
A019	Draft Legal Pages	Privacy Policy, Cookie Policy, Terms of Use.
A020	Marketing & Legal Content Review	Final approval of all content by Marketing Lead and Legal.
A021	Set Up Dev / Staging / Prod Environments	Provision and configure all environments and CI/CD.
A022	Configure CMS	Content types, roles, and editor workflow in the CMS.
A023	Build Component Library	Reusable components per the design system.
A024	Build Page Templates	Home, services, case study, directory, blog templates.
A025	Develop Backend APIs	Form handling; consultant-directory search; admin endpoints.
A026	Implement CRM Integration	Form-to-CRM connector with logging and retry.
A027	Configure Search & Analytics	Site search; Google Analytics; tag manager; dashboards.
A028	Develop Test Plan	Test plan and test cases mapped to RTM.
A029	Execute Functional Tests	Run all functional test cases; log defects.
A030	Execute Performance Tests	Lighthouse / WebPageTest performance test report.
A031	Conduct Accessibility Audit	Third-party WCAG 2.1 AA audit.
A032	Resolve Defects	Close all Sev-1 / Sev-2 defects; regression test.
A033	Conduct UAT	Sponsor and Marketing Lead-led acceptance testing.
A034	Final UAT Sign-off	Sponsor signs Formal Acceptance for UAT.
A035	Develop Launch Communications Plan	Internal announcement and external press / social assets.
A036	Migrate Content from Legacy Site	Move case studies and selected blog content into new CMS.
A037	Pre-Launch Internal Communications	Notify internal stakeholders of cutover plan.
A038	Production Cutover (Go-Live)	DNS update, SSL validation, smoke tests on production.

ID	Activity	Description of Work
A039	Post-Launch Hypercare	Two-week active monitoring and rapid-fix support.
A040	CMS Training for Marketing	Four-hour CMS training session; quick-reference guide.
A045	Operations Handoff	Runbooks, monitoring config, signed handoff document.

3

Assumption Log

Record of project assumptions and constraints, with owners and status.

ASSUMPTION LOG

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 5, 2026

ID	Category	Assumption / Constraint	Responsible Party	Due Date	Actions	Status	Comments
A-01	Resources	The 3 assigned core team members (Bob, Bill, Christine) will be available at planned allocations through project close.	Andrew	Ongoing	Confirm allocations with functional managers monthly.	Open	Critical to schedule baseline.
A-02	Schedule	The project can launch within approximately 6 months of charter approval.	Andrew	May 2026	Validate during schedule development.	Open	To be confirmed in planning.
A-03	Cost	$150,000 USD budget is sufficient to cover design, development, content, hosting, and contingency.	Mary	May 2026	Refine via bottom-up estimating in planning phase.	Open	Sponsor pre-approved figure.
A-04	Scope	Internal consultant portal and client workspaces are excluded; site is marketing-only.	Andrew	May 2026	Document explicitly in scope statement.	Open	Listed under project boundaries.
A-05	Stakeholders	Consultants worldwide will provide bios and case study content within agreed deadlines.	Christine	Aug 2026	Establish content collection plan and reminders.	Open	Risk to content readiness.
A-06	Technical	Existing CRM offers a supported integration method (API or connector) for lead capture.	Bob	Jun 2026	Verify CRM API access during requirements phase.	Open	Affects technical design.
A-07	Quality	WCAG 2.1 AA is the accepted accessibility standard for the site.	Bill	Jul 2026	Confirm with sponsor / legal counsel.	Open	Drives design and QA effort.
C-01	Constraint – Brand	Final brand and visual direction must be approved personally by the CEO (Mary).	Mary	Jul 2026	Schedule sponsor design review checkpoints.	Open	Single decision-maker = bottleneck risk.
C-02	Constraint – Budget	Total spend cannot exceed $150,000 USD without sponsor approval.	Andrew	Ongoing	Track via cost baseline and variance analysis.	Open	Hard cap from charter.
C-03	Constraint – Compliance	Site must comply with applicable data privacy regulations (e.g., GDPR) given Fortune 500 audience.	Bob	Sep 2026	Confirm requirements with legal during planning.	Open	Affects forms / cookies.

4

Basis of Estimates

Documentation of how each estimate was derived, including methods and ranges.

BASIS OF ESTIMATES – COST ESTIMATING WORKSHEET

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 14, 2026

Documents the estimating techniques used to derive activity cost estimates: parametric, analogous, and three-point. Bottom-up estimates are on the next page.

Parametric Estimates

ID	Cost Variable	Cost per Unit	Number of Units	Cost Estimate
A006	PM hours interviewing	$65/hr	30 hours	$1,950
A014	Writer hours per page	$50/hr	100 hours (~25 pages × 4 hrs)	$5,000
A015	Writer hours per case study	$50/hr	80 hours (20 cases × 4 hrs)	$4,000
A018	Stock images + headshots	$45/image avg.	50 images + photographer day	$2,200

Analogous Estimates

ID	Previous Activity	Previous Cost	Current Activity	Multiplier	Cost Estimate
A001	Charter (prior internal project)	$1,300	Develop Project Charter	1.0	$1,300
A011	Brand refresh (prior project)	$6,500	Develop Visual / Brand Design	1.2	$7,800
A031	Prior WCAG audit	$4,000	Conduct Accessibility Audit	1.0	$4,000
A039	Prior site launch hypercare	$5,000	Post-Launch Hypercare	1.0	$5,120

Three-Point (PERT) Estimates

ID	Optimistic	Most Likely	Pessimistic	Equation	Expected Cost
A024	$6,500	$7,200	$10,500	(O+4M+P)/6	$7,633
A025	$7,500	$8,640	$12,000	(O+4M+P)/6	$9,010
A032	$3,500	$4,320	$7,000	(O+4M+P)/6	$4,630

PERT (beta) weighting: tE = (O + 4M + P) / 6. Used for activities with significant uncertainty.

BASIS OF ESTIMATES – BOTTOM-UP COST ESTIMATING

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 14, 2026

Bottom-up estimate decomposes selected work packages into cost components: labor, material, supplies, equipment, travel, other direct costs (ODC), indirect costs, and reserve.

ID	Labor Hrs	Labor Rate	Total Labor	Material	Supplies	Equipment	Travel	Other Direct	Indirect	Reserve	Estimate
A003	60	$65/hr	$3,900	—	—	—	—	—	$390	$200	**$4,490**
A011	120	$65/hr	$7,800	$400	—	—	—	—	$780	$500	**$9,480**
A018	40	$65/hr	$2,600	$2,200	—	—	—	—	$260	$200	**$5,260**
A022	60	$72/hr	$4,320	$3,000	—	—	—	—	$432	$300	**$8,052**
A024	100	$72/hr	$7,200	$2,500	—	—	—	—	$720	$500	**$10,920**
A025	120	$72/hr	$8,640	—	—	—	—	—	$864	$500	**$10,004**
A031	40	$65/hr	$2,600	$4,000	—	—	—	—	$260	$300	**$7,160**
A038	16	$72/hr	$1,152	$1,200	—	—	—	—	$115	$100	**$2,567**

Indirect costs at 10% of direct labor (firm-standard overhead). Activity-level reserve covers uncertainty in the individual estimate; project-level contingency is tracked separately on the Activity Cost Estimates form.

BASIS OF ESTIMATES – SUMMARY NARRATIVE

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 14, 2026

Approach

Cost estimates were developed bottom-up from the Activity List using a combination of parametric, analogous, and three-point (PERT) techniques. Labor costs were derived from effort-hour estimates × blended firm-standard rates. Physical (non-labor) costs reflect quoted vendor SOWs and licensing prices current as of May 2026.

Source of Information

- Effort hours from the Activity Attributes / Duration Estimates documents.
- Labor rates from the firm's FY2026 internal blended-rate schedule: PM $65/hr, Web Developer $72/hr, UX Designer $65/hr, Content Strategist $50/hr.
- Vendor pricing from preliminary SOWs (frontend contractor, WCAG audit, hosting/CMS, photography).
- Analogous baselines from two prior internal projects (brand refresh 2024, marketing site refresh 2023).

Assumptions

- Internal labor billed at fully-loaded rates (salary + benefits + overhead).
- Vendor SOWs are fixed-price; no scope expansion expected during execution.
- Hosting fees included only for the project period; year-2 onward sit in run-rate operations.
- No travel costs anticipated; consultants engage remotely.
- U.S. dollar pricing throughout; no currency-conversion risk.

Constraints

- Hard cap of $150,000 USD set by the project charter.
- PM authority limited to $5,000 per item; anything larger requires sponsor approval.
- Vendor selections constrained to the firm's approved supplier list.

Estimate Range & Confidence

Overall project estimate is in the **Definitive (-5%/+10%)** range. Highest-confidence items are vendor SOWs with quoted prices (fixed). Lowest-confidence items are activities estimated three-point: Build Page Templates (A024), Backend APIs (A025), and Defect Resolution (A032), where uncertainty in scope and discovery risk is real.

Risks & Reserves

Contingency reserve: $15,000 (≈10% of direct estimate) is held by the PM for known-unknown risks identified in the Risk Register (e.g., CRM integration complexity, content readiness delays).
Management reserve: $7,500 is held by the Sponsor for unknown-unknowns and sits outside the cost baseline.

Approval
The cost baseline of **$142,952** ($127,952 direct estimate + $15,000 contingency) is recommended for sponsor approval. Adding the $7,500 management reserve (held outside the cost baseline by the sponsor) brings total funding required to **$150,452** — within the $150,000 charter cap (rounded). The Sponsor (Mary) approves the cost baseline before it is locked.

5

Change Log

Comprehensive list of changes submitted, evaluated, and their disposition.

CHANGE LOG

Project Title:	Mary's Consulting – New Company Website	**Date Prepared:**	Updated continuously; snapshot Oct 17, 2026

Master log of all change requests received on the project. Each request is tracked from submission through disposition. The log itself is an Organizational Process Asset for future projects.

ID	Category	Description of Change	Requestor	Submission Date	Status	Disposition	Disp. Date
CR-001	Schedule	Move kickoff meeting from Apr 28 to May 8 to accommodate sponsor calendar.	Andrew (PM)	Apr 25, 2026	**Closed**	**Approved**	Apr 25, 2026
CR-002	Documents	Update Project Charter to reflect revised kickoff date.	Andrew (PM)	Apr 26, 2026	**Closed**	**Approved**	Apr 26, 2026
CR-003	Scope	Add real-time chat widget to website (third-party integration).	Sales Lead	Jul 12, 2026	**Closed**	**Rejected**	Jul 18, 2026
CR-004	Scope	Add LinkedIn-link field to consultant directory.	Sales Lead	Aug 28, 2026	**Closed**	**Deferred (Phase 2)**	Aug 28, 2026
CR-005	Cost	Negotiate 5-seat legacy CMS pricing in year 1; 10-seat from year 2.	Bob (Tech Lead)	Aug 22, 2026	**Closed**	**Approved**	Aug 22, 2026
CR-006	Quality	Update brand color tokens to fix WCAG contrast issues found in pre-audit.	Bill (UX)	Sep 4, 2026	**Closed**	**Approved**	Sep 4, 2026
CR-007	Scope, Cost, Schedule	Add Press / Media section to website (2 pages, 15 items at launch).	Mary (Sponsor)	Sep 13, 2026	**Closed**	**Approved**	Sep 16, 2026
CR-008	Scope, Requirements, Cost	Add LinkedIn icons linking to consultant profiles on each bio card (~50 launch).	Marketing Lead	Oct 15, 2026	**Closed**	**Approved**	Oct 17, 2026

Summary: 8 change requests received. **6 Approved**, **1 Rejected**, **1 Deferred** to Phase 2. All requests dispositioned within the timing required by the Change Management Plan (within 5 business days of submission).

6

Cost Estimates

Quantitative cost estimates for each activity in the activity list.

ACTIVITY COST ESTIMATES

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 14, 2026

WBS	ID	Resource	Labor Costs	Physical Costs	Estimate Method	Range	Confidence
1.1.1	A001	Andrew (PM)	$1,300	—	Analogous	±20%	Medium
1.1.1	A002	Andrew (PM)	$1,040	—	Analogous	±20%	Medium
1.1.2	A003	Andrew (PM)	$3,900	—	Analogous	±20%	Medium
1.1.2	A004	Andrew (PM)	$1,300	—	Analogous	±20%	Medium
1.1.4	A005	Andrew (PM)	$2,600	—	Analogous	±20%	Medium
1.2.1	A006	Andrew (PM)	$1,950	—	Parametric	±10%	High
1.2.1	A007	Andrew (PM)	$1,040	—	Analogous	±20%	Medium
1.2.1	A008	Christine	$600	—	Parametric	±10%	High
1.2.2	A009	Andrew (PM)	$2,600	—	Three-point	±15%	Medium
1.2.3	A010	Bill (UX)	$3,250	—	Three-point	±15%	Medium
1.2.4	A011	Bill (UX)	$7,800	$400 Design tools / fonts license	Three-point	±15%	Medium
1.2.5	A012	Mary (Sponsor)	$0	—	Analogous	±20%	Medium
1.3.1	A013	Christine	$1,500	—	Analogous	±20%	Medium
1.3.2	A014	Christine	$5,000	—	Parametric	±10%	High
1.3.3	A015	Christine	$4,000	$500 Client clearance / legal review fee	Three-point	±15%	Medium
1.3.4	A016	Christine	$3,000	—	Parametric	±10%	High
1.3.5	A017	Christine	$2,000	—	Parametric	±10%	High
1.3.6	A018	Bill (UX)	$2,600	$2,200 Stock imagery + photographer fees	Analogous	±20%	Medium
1.3.7	A019	Andrew (PM)	$1,040	—	Analogous	±20%	Medium
1.3.2	A020	Andrew (PM)	$1,560	—	Analogous	±20%	Medium
1.4.1	A021	Bob (Dev)	$2,880	$800 Cloud env. setup / dev tooling	Analogous	±20%	Medium
1.4.2	A022	Bob (Dev)	$4,320	$3,000 CMS license (annual)	Three-point	±15%	Medium
1.4.3	A023	Bob (Dev)	$5,760	—	Three-point	±15%	Medium
1.4.3	A024	Bob (Dev)	$7,200	$2,500 Frontend contractor SOW	Three-point	±15%	Medium
1.4.4	A025	Bob (Dev)	$8,640	—	Three-point	±15%	Medium
1.4.5	A026	Bob (Dev)	$4,320	—	Three-point	±15%	Medium

WBS	ID	Resource	Labor Costs	Physical Costs	Estimate Method	Range	Confidence
1.4.6	A027	Bob (Dev)	$2,880	$400 Analytics tooling	Analogous	±20%	Medium
1.5.1	A028	Andrew (PM)	$1,300	—	Analogous	±20%	Medium
1.5.2	A029	Bob (Dev)	$4,320	—	Three-point	±15%	Medium
1.5.3	A030	Bob (Dev)	$2,160	—	Analogous	±20%	Medium
1.5.4	A031	Bill (UX)	$2,600	$4,000 Third-party WCAG audit fee	Analogous	±20%	Medium
1.5.6	A032	Bob (Dev)	$4,320	—	Three-point	±15%	Medium
1.5.5	A033	Andrew (PM)	$2,600	—	Three-point	±15%	Medium
1.5.5	A034	Mary (Sponsor)	$0	—	Analogous	±20%	Medium
1.6.1	A035	Christine	$800	—	Analogous	±20%	Medium
1.6.2	A036	Christine	$2,000	—	Parametric	±10%	High
1.6.1	A037	Christine	$400	—	Analogous	±20%	Medium
1.6.3	A038	Bob (Dev)	$1,152	$1,200 Hosting Q4 / SSL / CDN	Analogous	±20%	Medium
1.6.4	A039	Bob (Dev)	$4,320	$800 Hypercare on-call coverage	Analogous	±20%	Medium
1.6.6	A040	Christine	$800	—	Analogous	±20%	Medium
1.6.5	A045	Andrew (PM)	$1,300	—	Analogous	±20%	Medium
Subtotal			**$112,152**	**$15,800**			**$127,952**
Contingency Reserve					Reserve analysis	10%	**$15,000**
Cost Baseline							**$142,952**
Management Reserve (sponsor-held)					Held outside cost baseline		**$7,500**
Total Funding Required							**$150,452**

Range and confidence reflect the estimating method used. See the Basis of Estimates document for the detailed estimating approach for each activity.

7

Cost Forecast

Forecast of project costs based on Earned Value Analysis (EAC, VAC).

COST FORECAST

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Cost forecast based on Earned Value Analysis as of the most recent reporting period. Estimate at Completion (EAC) is calculated using EAC = BAC / CPI, assuming current cost performance continues. Variance at Completion (VAC) = BAC – EAC. BAC = $144,000 (Cost Baseline excluding Management Reserve).

Reporting Period	BAC	EV	AC	CPI	EAC	VAC	Forecast Status
End of Month 1	$144,000	$14,000	$14,500	0.97	$148,454	-$4,454	Slightly over
End of Month 2	$144,000	$32,000	$31,200	1.03	$140,400	+$3,600	Under budget
End of Month 3	$144,000	$58,000	$57,800	1.00	$144,497	-$497	On budget
End of Month 4	$144,000	$92,000	$93,500	0.98	$146,348	-$2,348	Slightly over
End of Month 5	$144,000	$128,000	$128,500	1.00	$144,562	-$562	On budget
End of Month 6 (Forecast)	$144,000	$144,000	$144,500	1.00	$144,500	-$500	Within tolerance

8

Duration Estimates

Estimated duration for each activity, with confidence ranges.

DURATION ESTIMATES

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

ID	Activity	Description	Effort (hrs)	Duration Estimate
A001	Develop Project Charter	Analogous est.	20	5 working days
A002	Identify Stakeholders	Analogous est.	16	3 working days
A003	Develop Subsidiary Plans	Analogous est.	60	12 working days
A004	Establish Baselines	Analogous est.	20	5 working days
A005	Project Closeout	Analogous est.	40	8 working days
A006	Conduct Requirements Interviews	Parametric est.	30	5 working days
A007	Run Requirements Focus Groups	Analogous est.	16	3 working days
A008	Distribute Consultant Questionnaire	Parametric est.	12	7 working days
A009	Document Requirements & RTM	Three-point est.	40	5 working days
A010	Develop Information Architecture	Three-point est.	50	7 working days
A011	Develop Visual / Brand Design	Three-point est.	120	15 working days
A012	Sponsor Design Review & Approval	Analogous est.	8	3 working days
A013	Develop Content Strategy	Analogous est.	30	4 working days
A014	Write Marketing Page Copy	Parametric est.	100	18 working days
A015	Produce Case Studies	Three-point est.	80	20 working days
A016	Collect Consultant Bios	Parametric est.	60	25 working days
A017	Write Blog Seed Content	Parametric est.	40	10 working days
A018	Source / License Imagery	Analogous est.	40	8 working days
A019	Draft Legal Pages	Analogous est.	16	4 working days
A020	Marketing & Legal Content Review	Analogous est.	24	5 working days
A021	Set Up Dev / Staging / Prod Environments	Analogous est.	40	5 working days
A022	Configure CMS	Three-point est.	60	7 working days
A023	Build Component Library	Three-point est.	80	12 working days
A024	Build Page Templates	Three-point est.	100	15 working days
A025	Develop Backend APIs	Three-point est.	120	12 working days
A026	Implement CRM Integration	Three-point est.	60	8 working days
A027	Configure Search & Analytics	Analogous est.	40	5 working days
A028	Develop Test Plan	Analogous est.	20	3 working days
A029	Execute Functional Tests	Three-point est.	60	8 working days
A030	Execute Performance Tests	Analogous est.	30	4 working days
A031	Conduct Accessibility Audit	Analogous est.	40	5 working days
A032	Resolve Defects	Three-point est.	60	8 working days
A033	Conduct UAT	Three-point est.	40	5 working days
A034	Final UAT Sign-off	Analogous est.	8	2 working days
A035	Develop Launch Communications Plan	Analogous est.	16	3 working days
A036	Migrate Content from Legacy Site	Parametric est.	40	5 working days
A037	Pre-Launch Internal Communications	Analogous est.	8	2 working days
A038	Production Cutover (Go-Live)	Analogous est.	16	1 working days
A039	Post-Launch Hypercare	Analogous est.	60	10 working days
A040	CMS Training for Marketing	Analogous est.	16	1 working days
A045	Operations Handoff	Analogous est.	20	3 working days

9

Issue Log

Log of project issues with owner, status, severity, and resolution.

ISSUE LOG

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	Updated Sep 14, 2026

ID	Type	Description	Pri.	Impact on Objectives	Owner	Status	Res. Date	Resolution	Comments
I-001	Resource	Bill (UX) had unexpected medical leave Aug 10–14. Brand-design work delayed.	**High**	Schedule (1-week slip risk)	Andrew (PM)	**Resolved**	Aug 17, 2026	Bill returned with overlapping work re-prioritized; no net schedule slip. Backup designer briefed in case of recurrence.	Cross-training added to action items.
I-002	Technical	Approved CMS provider's enterprise tier no longer offers 5-seat licensing — only 10-seat.	**Medium**	Cost (+$1,000)	Bob (Dev)	**Resolved**	Aug 22, 2026	Negotiated 5-seat legacy pricing for first year; 10-seat from year 2.	Year-2 cost flagged for budgeting.
I-003	Stakeholder	Marketing Lead requested earlier visibility into design mockups (before sponsor review).	**Low**	Stakeholder engagement only	Bill (UX)	**Resolved**	Aug 5, 2026	Bill added Marketing Lead to weekly design review meetings.	Improved alignment going forward.
I-004	Scope	Sales Lead asked whether the consultant directory could include LinkedIn links.	**Low**	Scope (small)	Andrew (PM)	**Resolved**	Aug 28, 2026	Added to Phase 2 backlog, not in scope for current launch. Sales Lead agreed.	Documented in Decision Log as out-of-scope.
I-005	Quality	Initial accessibility lint detected color-contrast issues on 3 components in the design system.	**High**	Quality (WCAG compliance)	Bill (UX)	**Resolved**	Sep 4, 2026	Bill updated brand colors; sponsor re-approved.	Linter now in CI to prevent recurrence.
I-006	Technical	CRM API does not expose 'industry vertical' field needed for lead routing per F-05.	**High**	Schedule (1-week slip on A025); Quality	Bob (Dev)	**In Progress**	—	Working with CRM vendor on field-mapping workaround. Fallback: collect vertical via form, store in CRM 'notes' field at launch.	Vendor call scheduled Sep 17.
I-007	Resource	Consultant bio submission rate at 38% vs. 60% target by Sep 12.	**Medium**	Scope (smaller directory at launch)	Christine	**In Progress**	—	Mary issued a second firm-wide reminder; tiered launch plan in place (top 50 at launch, remainder post-launch).	Trend monitored weekly.
I-008	External	Hosting vendor reported planned maintenance window on Nov 22 (2 days before Go-Live).	**High**	Schedule (Go-Live risk)	Bob (Dev)	**Escalated**	—	Escalated to vendor account team requesting either window deferral or guaranteed exit criteria. Awaiting response.	Escalated to Sponsor as a watchpoint.
I-009	Process	Editorial review queue building up — Christine bottlenecked.	**Medium**	Schedule (content track)	Christine	**In Progress**	—	Marketing Lead taking on review of marketing-tone copy; Christine focusing on case studies and bios.	Effective Sep 14.
I-010	Scope	Sponsor (Mary) requesting new Press / Media section for launch.	**High**	Scope, Cost, Schedule (per CR-007)	Andrew (PM)	**Open**	—	Change request CR-007 drafted; impact analysis complete; awaiting CCB disposition.	Disposition expected Sep 16.

Status legend: Open (just logged) · In Progress (actively being worked) · Resolved (closed with fix) · Escalated (raised to sponsor / external party for resolution)

10

Lessons Learned Register

Knowledge gained during the project that can benefit current and future projects.

LESSONS LEARNED REGISTER

Project Title:	Mary's Consulting – New Company Website	**Date Prepared:**	Updated continuously; snapshot Dec 1, 2026

Lessons captured throughout project execution and reviewed at each phase gate. To be transferred to the firm's organizational lessons-learned repository at project closeout. Each lesson includes the trigger (what prompted the learning), the lesson itself (actionable takeaway), and the responsible party for applying it on future projects.

ID	Category	Date	Trigger / Situation	Lesson Learned	Responsible Party	Comments
LL-001	Initiation	May 8, 2026	Sponsor (Mary) signed the charter same-day after a single 30-minute review.	**Brief executive sponsors with a one-page summary before the formal review.** The executive summary sent 2 days early made Mary's review purely confirmatory — she had already mentally processed the content. Recommend this as standard practice for any sponsor-approval meeting.	Andrew (PM)	Pattern reused for design and UAT approvals — same speed result.
LL-002	Stakeholder	Jun 18, 2026	Sales Lead initially scored Neutral on the stakeholder register; after early CRM-flow involvement, moved to Supportive.	**Engage downstream consumers (Sales) of project outputs before they become demanders.** Inviting Sales Lead to define lead-quality criteria turned a Neutral stakeholder into a Supportive one and prevented post-launch scope fights.	Andrew (PM)	Replicate for any project where Marketing delivers to Sales.
LL-003	Requirements	Jul 2, 2026	Consultant focus group revealed 3 Must-priority requirements not surfaced in interviews.	**Combine interviews with focus groups for user-research breadth.** Interviews captured individual preferences; focus groups surfaced items that only emerged when consultants discussed with each other (e.g., bio consistency).	Andrew (PM)	Worth the extra week of elapsed time.
LL-004	Design	Aug 7, 2026	Sponsor's design feedback came back faster than planned (2 days vs. 5).	**Have the designer present design reviews in person to the sponsor.** Bill walked Mary through the brand decisions live; questions and approvals happened in the same meeting. Email-only design reviews would have stretched this to a week of back-and-forth.	Bill (UX)	Critical-path activity; saved 3 days.
LL-005	Quality	Aug 26, 2026	Pre-audit found only 4 Sev-3 contrast issues (prior projects averaged 20+).	**Build accessibility linting into CI from day one — don't defer to a final audit.** Catching issues at PR time costs ~5 minutes per fix; catching at audit time costs ~2 hours per fix plus rework risk. ROI was extraordinary.	Bob (Dev) / Bill (UX)	Make this firm-standard for all web projects.
LL-006	Risk	Sep 8, 2026	CRM API gap (no 'industry vertical' field) discovered during integration build.	**Schedule vendor technical-discovery calls BEFORE finalizing build estimates.** A 1-hour vendor call in week 1 of build would have revealed the field gap and let us plan the workaround upfront. Instead we discovered it mid-build and lost 5 days.	Bob (Dev)	Add to firm's procurement-strategy template.
LL-007	Stakeholder	Sep 14, 2026	Consultant bio submission rate stuck at 38% vs. 60% target by week 2.	**Distributed-stakeholder commitments need a named executive sponsor and tiered execution.** The first firm-wide email got a soft response. Mary's personally signed second nudge plus a tiered launch plan (top 50 at launch, remainder later) recovered the situation. Plan for this from day one in similar projects.	Christine	Tiered launch should be the default approach.

ID	Category	Date	Trigger / Situation	Lesson Learned	Responsible Party	Comments
LL-008	Communication	Sep 14, 2026	Editorial review queue bottlenecked on Christine; Marketing Lead absorbed marketing-tone copy review.	**Identify single-point review bottlenecks early and partition the queue.** Splitting review work between Christine (case studies + bios) and Marketing Lead (marketing-tone copy) doubled throughput overnight. Should have done this at content-strategy phase, not week 19.	Christine / Marketing Lead	Add to content-strategy template.
LL-009	Procurement	Sep 16, 2026	Frontend contractor (WebCraft Studios) delivered all milestones on or before due dates.	**Pre-paying 25% to lock contractor schedule is worth it for short engagements.** Made WebCraft prioritize our work; protected the build-phase critical path. Cost ~$625 of working capital tied up for 90 days; payoff was much greater.	Andrew (PM)	Negotiate this term in vendor SOWs by default.
LL-010	Risk	Sep 16, 2026	Sponsor-approval-delay risk (R-04) was originally rated Critical but never materialized.	**Pre-booking sponsor calendar slots and pre-briefing turns the highest sponsor-related risk into a non-event.** This pattern (LL-001, LL-004, LL-010 all relate) should be elevated to a firm-standard risk mitigation.	Andrew (PM)	Cross-references LL-001 and LL-004.
LL-011	Build	Sep 30, 2026	Performance budget enforced in CI prevented two regressions before they reached the performance test in A030.	**Performance budgets in CI are as valuable as automated tests.** They prevent slow code from being merged in the first place — much cheaper than diagnosing and fixing performance regressions later.	Bob (Dev)	Add to firm's CI/CD reference architecture.
LL-012	Planning	Oct 9, 2026	Three-point estimates on build activities (A024, A025, A032) all came in within ±5% of expected duration.	**Three-point estimating works when the team has prior experience with the activity type.** Bob's PERT estimates for build activities were highly accurate; Christine's estimates for bio collection (a novel activity for the firm) had much wider variance. Use 3-point only where the team has informed pessimism.	Andrew (PM)	For novel activities, use higher-uncertainty techniques (e.g., wide ranges, rolling-wave).
LL-013	Test	Nov 17, 2026	UAT completed in 5 days vs. 7 planned, with zero Sev-1/2 findings.	**UAT goes faster when sponsors and SMEs are given written test scenarios in advance.** We sent Mary and the Marketing Lead a 1-page script of 'try these flows' the day before. Their feedback was focused and specific rather than wandering exploration. Consider scripted + exploratory mix.	Andrew (PM)	Saved 2 days on critical path.
LL-014	Launch	Nov 24, 2026	Production cutover happened on a Tuesday with zero incidents.	**Schedule production cutovers Tuesday–Thursday for full vendor-support availability.** Tuesday cutover meant the hosting vendor had full staffing on standby and we had 3 business days of hypercare attention before the weekend. Friday cutovers (often pressured by 'hit the month-end target') frequently fail for exactly the opposite reasons.	Bob (Dev)	Make this a firm-standard cutover policy.

Total lessons captured: 14 across all phases. **Recurring patterns:** sponsor pre-briefing (LL-001, LL-004, LL-010); single-point bottlenecks (LL-008); engaging downstream stakeholders early (LL-002, LL-003). These patterns will be elevated to firm-standard practices at closeout.

11

Milestone List

Significant points or events in the project, with target dates.

MILESTONE LIST

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

#	Milestone	Description	Type	Target Date
M01	Project Charter Approved	Sponsor signs the project charter; project formally authorized.	Major	May 08, 2026
M02	Planning Complete; Baselines Locked	All subsidiary plans drafted; scope, schedule, and cost baselines approved by the sponsor.	Major	Jun 08, 2026
M03	Requirements Approved	Requirements Documentation and RTM approved; entry to design phase.	Phase Gate	Jul 02, 2026
M04	Design Approved by Sponsor	Mary signs off personally on the visual brand package; entry to build phase.	Phase Gate	Aug 07, 2026
M05	All Content Approved	All marketing copy, case studies, bios, blog seed, imagery, and legal pages reviewed and approved.	Phase Gate	Aug 26, 2026
M06	Build Complete (Alpha)	All build activities (CMS, components, templates, backend, CRM, search, analytics) complete.	Phase Gate	Oct 09, 2026
M07	Functional Testing Complete	All Must-priority functional test cases executed.	Major	Oct 22, 2026
M08	Accessibility Audit Passed	Third-party WCAG 2.1 AA audit returns zero Sev-1 findings.	Major	Oct 09, 2026
M09	UAT Sign-off	Sponsor and Marketing Lead sign UAT acceptance.	Phase Gate	Nov 19, 2026
M10	Production Go-Live	Site live on marysconsulting.com; smoke tests pass.	Major	Nov 24, 2026
M11	Hypercare Complete	Two-week hypercare window completed; site stable.	Major	Dec 10, 2026
M12	Operations Handoff Signed	IT/Hosting Operations signs handoff document.	Major	Dec 15, 2026
M13	Project Closed	Lessons learned filed; formal acceptance signed; project records archived.	Major	Dec 29, 2026

Type: 'Major' = key project milestones; 'Phase Gate' = transitions between phases requiring formal review/approval.

12

Physical Resources Assignments

Assignment of non-human resources (hardware, software, facilities, services).

PHYSICAL RESOURCES ASSIGNMENTS

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Physical (non-human) resources assigned to the project, including hardware, software licenses, hosting, services, and facilities. Quantities and assignment windows align with the Resource Management Plan and Resource Breakdown Structure.

Resource	Type	Quantity	Assigned To / Phase	Source	Cost
AWS hosting (Prod + Staging)	Cloud Infra	1 account	Build → Closeout	AWS	$3,200
WordPress Enterprise license	Software	1 site	Build → Closeout	WordPress VIP	$6,000
HubSpot CRM connector	Software	1 license	Build → Closeout	HubSpot	$2,400
Figma Organization seats	Software	4 seats	Design → Launch	Figma	$720
Jira + Confluence	Software	8 users	All phases	Atlassian	$960
GitHub Team	Software	8 users	Build → Closeout	GitHub	$384
SSL/TLS certificate (EV)	Service	1	Launch → Closeout	DigiCert	$300
Stock photo subscription	Content	1	Content & Design	Shutterstock	$500
Pen-test engagement	Service	1	Test phase	ExternalSec Co.	$8,000
Conference room (HQ)	Facility	Recurring	All phases	Internal	$0

13

Project Calendars

Working days, shifts, and non-working time for the project and resources.

PROJECT CALENDAR

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

Working days are Monday–Friday excluding U.S. federal holidays. Weekends and holidays are non-working days for the project. Key project dates and milestones are marked.

May 2026

S	M	T	W	T	F	S
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

June 2026

S	M	T	W	T	F	S
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

July 2026

S	M	T	W	T	F	S
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

August 2026

S	M	T	W	T	F	S
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Legend: White = working day | Grey = weekend | Pink = holiday | Yellow = milestone

September 2026

S	M	T	W	T	F	S
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

October 2026

S	M	T	W	T	F	S
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

November 2026

S	M	T	W	T	F	S
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

December 2026

S	M	T	W	T	F	S
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

Legend: White = working day Grey = weekend Pink = holiday Yellow = milestone

14

Project Communications

Record of formal project communications produced and distributed.

PROJECT COMMUNICATIONS

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Record of formal project communications produced and distributed. Items below have been issued; future communications follow the cadence defined in the Communications Management Plan.

Date	Communication	Type	From	To	Channel
May 8, 2026	Kick-off Meeting Deck	Presentation	Andrew	All stakeholders	MS Teams + Email
May 15, 2026	Charter Sign-off Notice	Email	Andrew	Mary, Core Team	Email
Weekly (Mondays)	Project Status Report	Report	Andrew	Mary, Marketing, IT	Email + SharePoint
Bi-weekly (Fridays)	Sprint Demo Recording	Video	Andrew	Sponsor, Marketing	SharePoint
Monthly	Steering Committee Update	Presentation	Andrew	Mary, VPs	Live + Recording
Ad hoc	Risk Escalation	Email	Andrew	Mary	Email (high priority)
Ad hoc	Change Request Notification	Email	Andrew	CCB members	Email
Daily (during Build)	Stand-up Notes	Note	Andrew	Core team	Slack #mc-website
Phase end	Phase Gate Review Pack	Presentation	Andrew	Sponsor + CCB	Live meeting
At launch	Go-Live Announcement	Email + Web	Mary	Company-wide + Clients	Email + Intranet


15

Project Schedule

Time-phased plan showing planned dates for activities and milestones.

PROJECT SCHEDULE – GANTT CHART

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

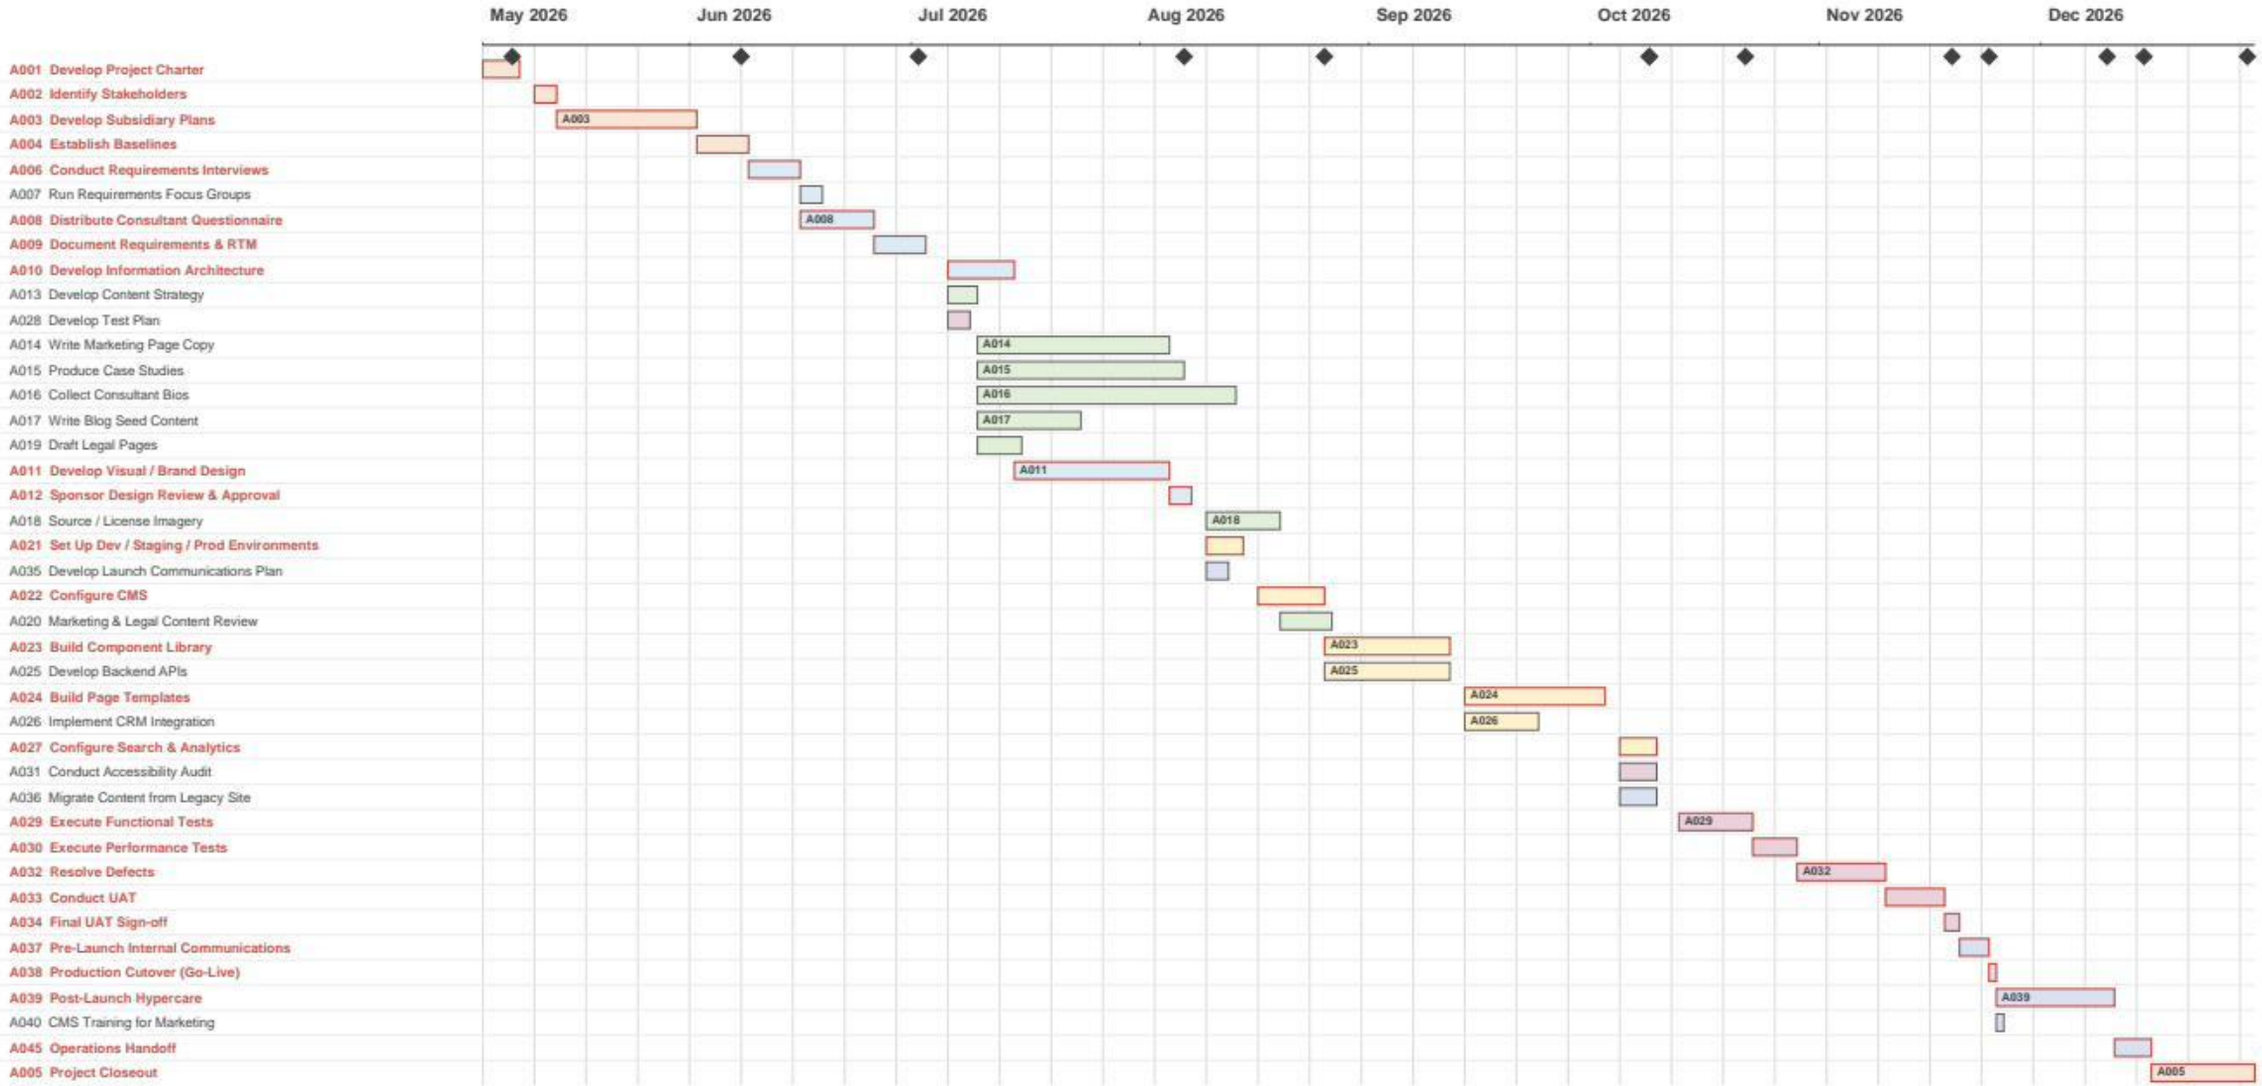

Red outline / red text = Critical Path	◆ = Milestone	Bar color = Major Deliverable (see WBS)

16


Project Schedule Network Diagram

Graphical representation of the logical relationships among activities.

PROJECT SCHEDULE NETWORK DIAGRAM

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 12, 2026

Activities are arranged in swim-lanes by Major Deliverable. Arrows indicate finish-to-start dependencies (default). Critical path activities are outlined in red.

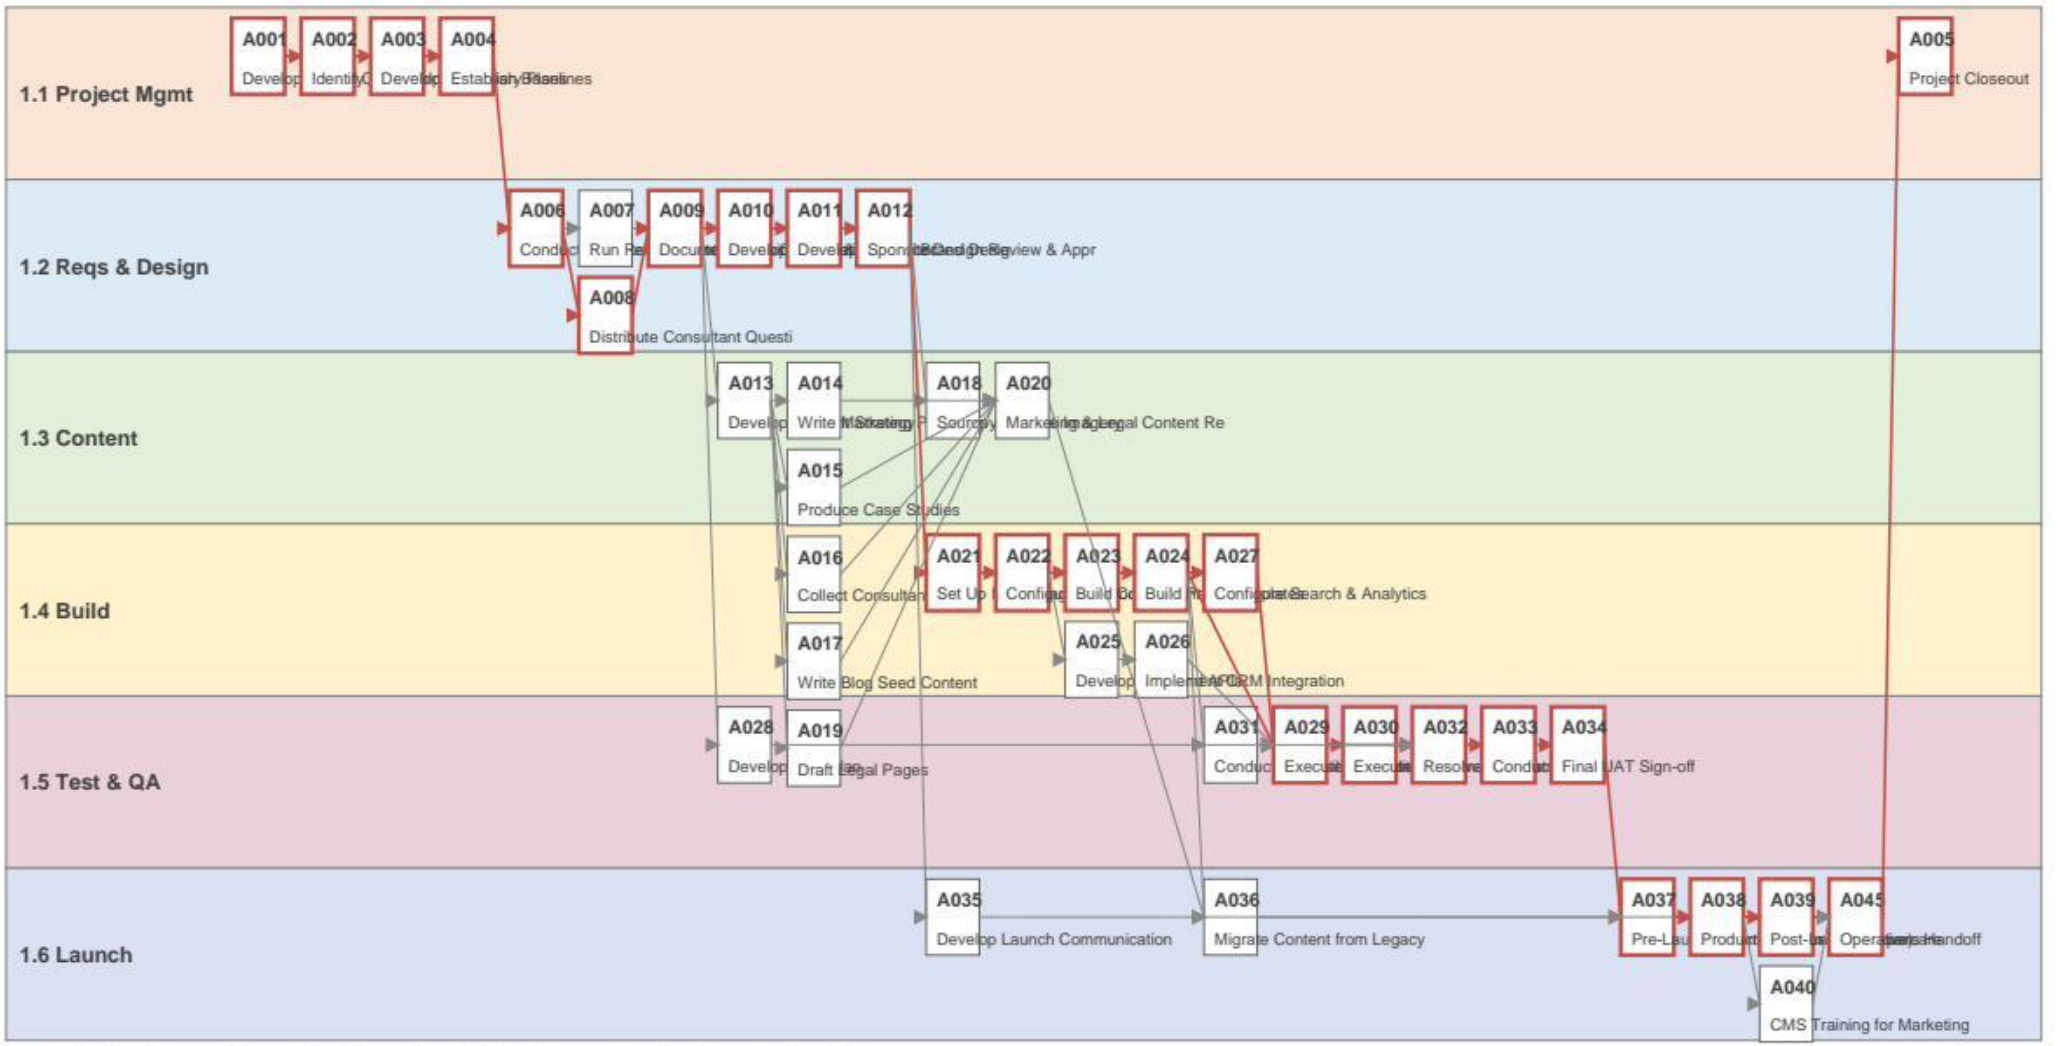

17

Project Scope Statement

Description of project scope, deliverables, exclusions, and acceptance criteria.

PROJECT SCOPE STATEMENT

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 9, 2026

Project Scope Description

Design, develop, and launch a new public-facing marketing website for Mary's Consulting at marysconsulting.com. The site will replace the current legacy site and serve as the firm's primary digital storefront for Fortune 500 buyers. It will include an updated brand identity, a service catalog covering project management consulting, a consultant directory of 500+ global consultants, a case-study library, a thought-leadership blog, and a Contact / Request-for-Proposal lead-capture flow integrated with the company CRM. The site will be responsive (desktop, tablet, mobile), WCAG 2.1 AA accessible, GDPR compliant, and managed via a CMS that allows non-technical staff to publish content without engineering involvement.

Project Deliverables

1. **Approved brand and visual design system** – brand guidelines, color palette, typography, component library.
2. **Information architecture and wireframes** – sitemap, page templates, interaction flows.
3. **Content set** – home, services, case studies (≥ 20), consultant directory entries, blog seed content (≥ 10 posts), legal pages.
4. **CMS-driven website** – fully developed responsive site with editor workflow.
5. **CRM integration** – contact and RFP forms routed to the company CRM via API with logging and retry.
6. **Hosting environment** – production hosting, DNS, SSL, CDN, monitoring, and backup.
7. **Test & QA artifacts** – test plan, executed test cases, performance report, third-party WCAG 2.1 AA audit report.
8. **Production launch** – Go-Live event, post-launch support transition.
9. **Project management documents** – charter, plans, logs, status reports, lessons learned, formal acceptance.

Product Acceptance Criteria

- All Must-priority requirements verified and validated as documented in the Requirements Traceability Matrix.
- 75th-percentile Largest Contentful Paint (LCP) < 2.5 seconds in the pre-launch performance test.
- Third-party WCAG 2.1 AA audit returns zero Severity-1 findings.
- User Acceptance Testing completed with no open Severity-1 or Severity-2 defects.
- CEO (Mary) signs off on brand/visual fit.
- Marketing Lead signs off on content and CMS workflow.
- Legal/Compliance signs off on GDPR and accessibility.
- Production hosting documented and handed off to IT/Hosting Operations.

Project Exclusions

The following items are explicitly **OUT OF SCOPE** for this project:

- Internal consultant portal (extranet, time tracking, client workspaces).
- Client project delivery tools, dashboards, or collaboration spaces.
- Billing, invoicing, or financial-system integration.
- Paid advertising campaigns, SEO content production beyond launch seed, and ongoing marketing operations.
- Multi-language translation of consultant bios at launch (deferred to a future phase).
- Mobile native applications (iOS / Android).
- Migration of historical blog content older than 24 months.

PROJECT SCOPE STATEMENT

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 9, 2026

Project Constraints

Budget: Total project cost capped at $150,000 USD. Any expenditure beyond this requires sponsor approval.
Schedule: Production launch must occur on or before the November 2026 Go-Live milestone.
Resources: Core team is fixed at the Project Manager (Andrew) plus three team members (Bob, Bill, Christine). Functional manager approval is required to add resources.
Brand approval: Final brand and visual direction must be approved personally by the CEO (Mary). No delegation of this approval is permitted.
Quality: Site must meet WCAG 2.1 AA, GDPR, and the firm's IT security standards. These are non-negotiable.
Technology: CMS selection must be from the firm's approved technology list; hosting must use the firm's approved cloud provider.
PM Authority: The PM may approve expenditures up to $5,000 per item and reallocate up to 10% within budget categories. Anything beyond requires sponsor approval.

Project Assumptions

- The three core team members will be available at planned allocations through project close.
- Mary will be available for design reviews at agreed checkpoints; turnaround on brand decisions ≤ 5 business days.
- The existing CRM offers a supported integration method (API or vendor connector) for lead capture.
- Consultants worldwide will provide updated bios and case-study content within agreed deadlines.
- WCAG 2.1 AA is the accepted accessibility standard for the project.
- Marketing will execute SEO and content campaigns post-launch to drive traffic; the project itself does not include those activities.
- The hosting/CMS vendor's standard SLA (≥ 99.5% uptime) is acceptable to IT Operations.
- No major change in the firm's service offerings during the project timeline.

18

Project Team Assignments

Documentation of which team members are assigned to which roles.

PROJECT TEAM ASSIGNMENTS

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Formal assignment of named individuals to project roles, including reporting line, allocation percentage, and start/end dates. All assignments confirmed by the resource manager and acknowledged by each team member.

Name	Role	Reports To	Allocation	Start	End	Location
Mary	Sponsor / CEO	Board	10%	May 8, 2026	Dec 31, 2026	HQ – New York
Andrew	Project Manager	Mary	100%	May 8, 2026	Dec 31, 2026	HQ – New York
Bob	Lead Developer	Andrew	100%	May 22, 2026	Dec 15, 2026	Remote – Austin
Bill	Developer / DevOps	Andrew	80%	Jun 1, 2026	Dec 15, 2026	Remote – Toronto
Christine	UX Designer / Content Lead	Andrew	100%	May 22, 2026	Dec 15, 2026	Remote – London
Marketing Lead (TBN)	Brand & Content Reviewer	Mary	20%	May 15, 2026	Dec 15, 2026	HQ – New York
IT Lead (TBN)	Security & Infra Reviewer	Mary	15%	May 15, 2026	Dec 15, 2026	HQ – New York
External Pen-Test Vendor	Security Auditor	Andrew	Fixed	Oct 1, 2026	Oct 15, 2026	External

19

Quality Control Measurements

Documented results of quality control activities.

QUALITY CONTROL MEASUREMENTS

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Documented results of quality control activities measuring deliverables against the Quality Metrics. Captured during the Test & QA phase and updated weekly during build sprints.

Metric ID	Metric	Target	Measured	Variance	Status	Action
QM-01	Page load time (LCP)	≤ 2.5 sec	2.1 sec	-0.4	Pass	None
QM-02	Lighthouse Accessibility Score	≥ 95	97	+2	Pass	None
QM-03	WCAG 2.1 AA compliance	100%	98%	-2%	Minor	Fix 3 alt-text issues
QM-04	Mobile responsiveness	100% pages	100%	0	Pass	None
QM-05	Defect density (per page)	≤ 0.5	0.3	-0.2	Pass	None
QM-06	UAT pass rate	≥ 95%	96%	+1%	Pass	None
QM-07	Critical defects open at Go-Live	0	0	0	Pass	None
QM-08	Browser compatibility (top 5)	100%	100%	0	Pass	None
QM-09	Form submission success rate	≥ 99%	99.4%	+0.4%	Pass	None
QM-10	SEO score (Ahrefs)	≥ 80	84	+4	Pass	None

20

Quality Metrics

Specific quality attributes and how they will be measured.

QUALITY METRICS

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 21, 2026

ID	Item	Metric	Measurement Method
QM-01	Accessibility	WCAG 2.1 AA findings	Third-party audit at A031; defect count by severity
QM-02	Performance – LCP	Largest Contentful Paint (75th percentile)	Lighthouse CI on 5 representative pages; target < 2.5s on 4G
QM-03	Performance – CLS	Cumulative Layout Shift (75th percentile)	Lighthouse CI; target < 0.1
QM-04	Defect density	Defects per page template	Count of Sev-1/Sev-2 defects ÷ 12 templates; target < 0.5
QM-05	Defect resolution time	Average days from logged → resolved	Jira report by severity; target Sev-1 < 2 days; Sev-2 < 5 days
QM-06	Code review coverage	% of PRs with peer-reviewed approval	GitHub branch protection; target 100%
QM-07	Test coverage	% lines covered by automated tests	Jest coverage report; target > 70% on JavaScript components
QM-08	Security – OWASP scan	Number of high/critical findings	ZAP / Burp scan before UAT; target 0 high/critical
QM-09	Content quality	% of pages signed off by Marketing Lead	Tracked in content QA log; target 100% before UAT
QM-10	Bio submission rate	% of in-scope consultants with submitted bio	Christine's tracker; target 60% by Sep 25
QM-11	Cross-browser	Browser/device combinations passing smoke tests	BrowserStack matrix: Chrome, Firefox, Safari, Edge × desktop+mobile; target 100%
QM-12	Uptime (post-launch)	Production availability during hypercare	Pingdom monitor; target ≥ 99.9% over 14-day hypercare window

21

Quality Report

Summary of quality management issues, recommendations, and corrective actions.

QUALITY REPORT

Project Title:	Mary's Consulting – New Company Website	**Date Prepared:**	Sep 30, 2026 (End of Sept.)

Reporting period: Sep 1–30, 2026. Output of Manage Quality. Used by the PM and Sponsor to make decisions about quality posture and corrective action.

Quality Status by Metric

ID	Metric	Current Measurement	Status
QM-01	Accessibility (WCAG 2.1 AA)	Pre-audit by Bill found 4 Sev-3 contrast issues, 0 Sev-1/2	On Track
QM-02	Performance – LCP	1.9s (75th-pct) on 4G	On Track
QM-03	Performance – CLS	0.04	On Track
QM-04	Defect density	0.6 Sev-1/Sev-2 defects per template	At Risk
QM-05	Defect resolution time	Sev-1: 1.5d avg; Sev-2: 4.2d avg	On Track
QM-06	Code review coverage	100% (47 PRs reviewed)	On Track
QM-07	Test coverage	62% on JS components	At Risk
QM-08	OWASP scan	1 medium finding (CSRF on form); 0 high/critical	On Track
QM-09	Content quality	78% of pages signed off so far	On Track
QM-10	Bio submission rate	44% (target 60% by Sep 25)	Off Track
QM-11	Cross-browser	Pending – will run after build complete (Oct)	Not Started
QM-12	Uptime (post-launch)	Not yet measurable	Not Started

Defect Summary (cumulative)

Total defects logged: 47
Resolved: 28
Open: 19 (0 Sev-1, 4 Sev-2, 13 Sev-3, 2 Sev-4)
Sev-1/2 trend: Decreasing — peaked at 8 in early September, now 4. Burn-down on track for UAT entry on Nov 10.
Defect categories: 38% UI/visual, 28% functional, 18% accessibility, 11% performance, 5% content.

Process Improvements & Recommendations

1. Bio submission (Off Track): Mary issued a second firm-wide nudge Sep 12. Recommend tiered launch (top 50 bios at launch, remainder Phase 2). Status: in progress; tracked as Issue I-007.
2. Test coverage (At Risk): Bob to dedicate 6 hours in Week 21 to write tests for the case-study and directory components — currently the lowest-covered.
3. Defect density (At Risk): Reflects scope-expansion from CR-007. PM accepts and continues to monitor; Sev-1/2 burn-down is healthy.
4. Lessons: Building a11y linting into CI from the start has paid off — only 4 Sev-3 contrast issues in pre-audit (vs. ~20 expected based on prior projects).

Quality Audit Findings (Sep 11 Phase Gate – Build Mid-Point)

Good practices: Component library reviewed and praised; CI quality gates working.
Improvements: Test coverage gaps; content-review queue bottleneck (now mitigated, see I-009).
Deficiencies: None Sev-1/2.
Audit form filed in /Quality/Audits/2026-09-11.pdf.

22

Requirements Documentation

Detailed documentation of how individual requirements meet business needs.

REQUIREMENTS DOCUMENTATION

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 8, 2026

ID	Requirement	Stakeholder	Category	Priority	Acceptance Criteria	Test / Verification	Phase / Release
B-01	Increase qualified inbound leads (MQLs) by 25% within 12 months of launch.	Mary (Sponsor)	Business	Must	Marketing analytics report shows ≥ 50 MQLs/month averaged over months 10–12 post-launch.	Analytics review	Post-launch
B-02	Reduce content-update cycle time from ~10 days to < 1 day.	Marketing Lead	Business	Must	Marketing can publish a new content page in < 1 business day end-to-end without IT involvement.	Demo + 30-day usage data	Launch
B-03	Position the brand credibly for Fortune 500 buyers.	Mary (Sponsor)	Business	Must	F500 buyer survey score ≥ 7.5 / 10 within 6 months.	Buyer survey	Post-launch
S-01	Marketing must be able to publish content without engineering involvement.	Marketing Lead	Stakeholder	Must	Editor role can create, preview, and publish a page using only the CMS UI.	User acceptance test	Build
S-02	Sales must receive new web-form leads in the CRM within 5 minutes of submission.	Sales Lead	Stakeholder	Must	End-to-end test from form submit to CRM record completes in ≤ 5 minutes for 100% of test cases.	Integration test	Build
S-03	Consultants must be able to submit/update their bio and case studies through a self-service form.	Consultant Community	Stakeholder	Should	Form requires ≤ 5 minutes to complete; submissions queue for editorial review.	Pilot with 10 consultants	Build
F-01	Provide a Contact / Request-for-Proposal form capturing name, work email, company, role, and message.	Marketing Lead	Functional	Must	All fields validated; submission stored and routed to CRM; thank-you confirmation displayed.	Functional test	Build
F-02	Display a searchable case-study library filterable by industry, service, and region.	Marketing Lead	Functional	Must	≥ 20 case studies at launch; filters return expected results for all combinations.	Functional test	Build
F-03	Provide a consultant directory searchable by industry, region, and language.	Marketing Lead	Functional	Should	All 500+ consultant bios appear; search returns expected results for all filters.	Functional test	Build
F-04	Provide a blog with categories, tags, author pages, and RSS feed.	Marketing Lead	Functional	Should	Editor can create, categorize, and tag posts; RSS feed validates.	Functional test	Build
F-05	Integrate the contact and RFP forms with the company CRM via documented API.	Sales Lead	Functional	Must	Lead records created in CRM with source-tracking fields populated; failures logged and retried.	Integration test	Build
N-01	All public pages must load in < 3 seconds on standard broadband (LCP < 2.5s).	Mary (Sponsor)	Non-functional	Must	75th-percentile LCP < 2.5s in pre-launch performance test.	Performance test (Lighthouse / WebPageTest)	Test
N-02	Site must achieve WCAG 2.1 AA accessibility compliance.	Legal / Compliance	Non-functional	Must	Third-party WCAG audit pass with zero Severity-1 findings.	Third-party accessibility audit	Test

ID	Requirement	Stakeholder	Category	Priority	Acceptance Criteria	Test / Verification	Phase / Release
N-03	Site must be responsive across desktop, tablet, and mobile (≥ 320px width).	Bill (UX)	Non-functional	Must	Visual review on top 5 device sizes shows no broken layouts or hidden content.	Visual / responsive test	Test
N-04	Site must remain available with 99.5% uptime SLA (monthly).	IT / Hosting Ops	Non-functional	Should	Hosting vendor contract specifies ≥ 99.5% SLA; monitoring confirms compliance.	SLA review	Operate
N-05	Site must comply with GDPR data privacy requirements.	Legal / Compliance	Non-functional	Must	Cookie consent, data subject rights, and privacy policy reviewed and approved by Legal.	Legal review	Test
T-01	Migrate existing case-study content from the legacy site to the new CMS.	Marketing Lead	Transition	Must	100% of case studies migrated with formatting verified by Marketing.	Content audit	Launch
T-02	Train Marketing team to use the new CMS.	Marketing Lead	Transition	Should	≥ 1 four-hour training session held; quick-reference guide delivered.	Training records	Launch

23

Requirements Traceability Matrix

Grid linking product requirements to the deliverables that satisfy them.

REQUIREMENTS TRACEABILITY MATRIX

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 8, 2026

Requirement Information					Relationship		Traceability	
ID	**Requirement**	**Source**	**Priority**	**Category**	**Business Objective**	**Deliverable**	**Verification**	**Validation**
B-01	Increase qualified inbound leads (MQLs) by 25% within 12 months of launch.	Mary (Sponsor)	Must	Business	Grow Fortune 500 client base	Live website + analytics dashboard	Analytics review	Quarterly benefits review with sponsor
B-02	Reduce content-update cycle time from ~10 days to < 1 day.	Marketing Lead	Must	Business	Modernize digital footprint	CMS with editor workflow	Demo + 30-day usage data	Marketing Lead sign-off
B-03	Position the brand credibly for Fortune 500 buyers.	Mary (Sponsor)	Must	Business	Grow Fortune 500 client base	Brand-aligned website	Buyer survey	Sponsor + Marketing review
S-01	Marketing must be able to publish content without engineering involvement.	Marketing Lead	Must	Stakeholder	Reduce content cycle time	CMS editor role	User acceptance test	Marketing UAT
S-02	Sales must receive new web-form leads in the CRM within 5 minutes of submission.	Sales Lead	Must	Stakeholder	Increase qualified leads	CRM integration	Integration test	Sales Lead sign-off
S-03	Consultants must be able to submit/update their bio and case studies through a self-service form.	Consultant Community	Should	Stakeholder	Modernize digital footprint	Consultant submission form	Pilot with 10 consultants	Pilot feedback
F-01	Provide a Contact / Request-for-Proposal form capturing name, work email, company, role, and message.	Marketing Lead	Must	Functional	Increase qualified leads	Contact / RFP form	Functional test	UAT
F-02	Display a searchable case-study library filterable by industry, service, and region.	Marketing Lead	Must	Functional	Position brand for F500	Case-study module	Functional test	UAT
F-03	Provide a consultant directory searchable by industry, region, and language.	Marketing Lead	Should	Functional	Modernize digital footprint	Consultant directory	Functional test	UAT
F-04	Provide a blog with categories, tags, author pages, and RSS feed.	Marketing Lead	Should	Functional	Position brand for F500	Blog module	Functional test	UAT
F-05	Integrate the contact and RFP forms with the company CRM via documented API.	Sales Lead	Must	Functional	Increase qualified leads	CRM integration	Integration test	UAT

Requirement Information					Relationship		Traceability	
ID	Requirement	Source	Priority	Category	Business Objective	Deliverable	Verification	Validation
N-01	All public pages must load in < 3 seconds on standard broadband (LCP < 2.5s).	Mary (Sponsor)	Must	Non-functional	Grow F500 client base	Optimized site	Performance test (Lighthouse / WebPageTest)	Performance audit
N-02	Site must achieve WCAG 2.1 AA accessibility compliance.	Legal / Compliance	Must	Non-functional	Compliance	Accessibility report	Third-party accessibility audit	Audit sign-off
N-03	Site must be responsive across desktop, tablet, and mobile (≥ 320px width).	Bill (UX)	Must	Non-functional	Modernize digital footprint	Responsive design	Visual / responsive test	QA review
N-04	Site must remain available with 99.5% uptime SLA (monthly).	IT / Hosting Ops	Should	Non-functional	Reliability	Hosting contract + monitoring	SLA review	Operations review
N-05	Site must comply with GDPR data privacy requirements.	Legal / Compliance	Must	Non-functional	Compliance	Privacy implementation	Legal review	Legal sign-off
T-01	Migrate existing case-study content from the legacy site to the new CMS.	Marketing Lead	Must	Transition	Modernize digital footprint	Migrated content	Content audit	Marketing sign-off
T-02	Train Marketing team to use the new CMS.	Marketing Lead	Should	Transition	Reduce content cycle time	Training materials	Training records	Marketing Lead sign-off

INTER-REQUIREMENTS TRACEABILITY MATRIX

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 8, 2026

Maps each business or stakeholder requirement (left side) to the technical / functional / non-functional / transition requirements (right side) that satisfy it.

Business / Stakeholder Requirement				Technical Requirement			
ID	**Business Requirement**	**Priority**	**Source**	**ID**	**Technical Requirement**	**Priority**	**Source**
B-01	Increase qualified inbound leads (MQLs) by 25% within 12 months of launch.	Must	Mary (Sponsor)				
B-02	Reduce content-update cycle time from ~10 days to < 1 day.	Must	Marketing Lead	F-03	Provide a consultant directory searchable by industry, region, and language.	Should	Marketing Lead
B-02	Reduce content-update cycle time from ~10 days to < 1 day.	Must	Marketing Lead	N-03	Site must be responsive across desktop, tablet, and mobile (≥ 320px width).	Must	Bill (UX)
B-02	Reduce content-update cycle time from ~10 days to < 1 day.	Must	Marketing Lead	T-01	Migrate existing case-study content from the legacy site to the new CMS.	Must	Marketing Lead
B-03	Position the brand credibly for Fortune 500 buyers.	Must	Mary (Sponsor)				
S-01	Marketing must be able to publish content without engineering involvement.	Must	Marketing Lead	T-02	Train Marketing team to use the new CMS.	Should	Marketing Lead
S-02	Sales must receive new web-form leads in the CRM within 5 minutes of submission.	Must	Sales Lead	F-01	Provide a Contact / Request-for-Proposal form capturing name, work email, company, role, and message.	Must	Marketing Lead
S-02	Sales must receive new web-form leads in the CRM within 5 minutes of submission.	Must	Sales Lead	F-05	Integrate the contact and RFP forms with the company CRM via documented API.	Must	Sales Lead
S-03	Consultants must be able to submit/update their bio and case studies through a self-service form.	Should	Consultant Community	F-03	Provide a consultant directory searchable by industry, region, and language.	Should	Marketing Lead
S-03	Consultants must be able to submit/update their bio and case studies through a self-service form.	Should	Consultant Community	N-03	Site must be responsive across desktop, tablet, and mobile (≥ 320px width).	Must	Bill (UX)
S-03	Consultants must be able to submit/update their bio and case studies through a self-service form.	Should	Consultant Community	T-01	Migrate existing case-study content from the legacy site to the new CMS.	Must	Marketing Lead

24

Resource Breakdown Structure

Hierarchical representation of resources by category and type.

RESOURCE BREAKDOWN STRUCTURE

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 18, 2026

Hierarchical decomposition of all project resources by category. Used for resource planning, allocation, and tracking.

- **1.1 People**
  - **1.1.1 Project Manager**
    - 1.1.1.1 Senior PM (1)
  - **1.1.2 Web Developer / Tech Lead**
    - 1.1.2.1 Senior Developer (1) – Bob
    - 1.1.2.2 Mid Frontend Contractor (1) – vendor
  - **1.1.3 UX / Visual Designer**
    - 1.1.3.1 Senior Designer (1) – Bill
  - **1.1.4 Content Strategist**
    - 1.1.4.1 Mid Content Strategist (1) – Christine
  - **1.1.5 Stakeholder / SME Time**
    - 1.1.5.1 Sponsor (Mary) – ~3% time
    - 1.1.5.2 Marketing Lead – ~5% time
    - 1.1.5.3 Sales Lead – ~3% time
    - 1.1.5.4 Legal / Compliance – ~10 hrs total
    - 1.1.5.5 IT / Hosting Operations – ~16 hrs total
- **1.2 Equipment / Infrastructure**
  - **1.2.1 Cloud Hosting Environments**
    - 1.2.1.1 Development environment (1)
    - 1.2.1.2 Staging environment (1)
    - 1.2.1.3 Production environment (1)
  - **1.2.2 CI/CD Pipeline Access (firm-standard)**
  - **1.2.3 Analytics & Monitoring Stack**
    - 1.2.3.1 Google Analytics 4 (free tier)
    - 1.2.3.2 Google Tag Manager (free tier)
    - 1.2.3.3 Uptime monitoring (firm-standard)
- **1.3 Materials / Digital Assets**
  - **1.3.1 Imagery**
    - 1.3.1.1 Stock images (~50, royalty-free)
    - 1.3.1.2 Consultant headshots (1-day shoot)
  - **1.3.2 Brand Assets**
    - 1.3.2.1 Brand fonts (commercial license)
    - 1.3.2.2 Logo files (existing firm assets)
- **1.4 Supplies / Services / Software**
  - **1.4.1 CMS License (annual, 5 seats)**
  - **1.4.2 WCAG 2.1 AA Audit (3rd-party service, 1 cycle)**
  - **1.4.3 Design Tools (Figma / Adobe – existing seats)**
  - **1.4.4 Project Management Tools (MS Project – existing)**
  - **1.4.5 SSL Certificate / CDN (annual)**
- **1.5 Locations / Facilities**
  - **1.5.1 Firm Office (hybrid – 1 day/week in-person)**
  - **1.5.2 Meeting Rooms (booked as needed)**
  - **1.5.3 Executive Boardroom (sponsor reviews)**

25

Resource Calendars

Availability of named resources during the project.

RESOURCE CALENDARS

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Availability of human and key physical resources by week. 'F' = full availability, 'P' = partial (≤50%), 'X' = unavailable / PTO, 'H' = holiday. Reflects approved time off and known commitments. Standard work week is 40 hours, Mon-Fri, EST core hours 10am–3pm.

Resource	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Notes
Andrew (PM)	F	F	F	P	F	F	F	F	PTO Aug 18–25
Bob (Lead Dev)	P	F	F	F	F	F	F	P	Starts May 22
Bill (Dev/DevOps)	X	F	F	F	F	F	F	P	Starts Jun 1; 80% allocation
Christine (UX/Content)	P	F	F	F	F	F	F	P	Starts May 22
Marketing Lead	P	P	P	P	P	P	P	P	20% allocation
IT Lead	P	P	P	P	P	P	P	P	15% allocation
AWS Hosting	F	F	F	F	F	F	F	F	24/7 SLA
Pen-Test Vendor	X	X	X	X	X	F	X	X	Engagement Oct 1–15
Holidays	—	—	Jul 4 H	—	Sep 7 H	—	Nov 26 H	Dec 25 H	US holidays observed

26

Resource Requirements

Types and quantities of resources required for each activity.

RESOURCE REQUIREMENTS

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 18, 2026

ID	Resource	Quantity	Assumptions	Comments
R-01	Project Manager (Andrew)	1 person, 50% allocation	Available throughout project; backup arranged for vacation.	PM is also a stakeholder for the firm.
R-02	Web Developer / Tech Lead (Bob)	1 person, 75% during build, 25% otherwise	Senior-level skill; full-stack capability assumed.	Critical-path resource; vacation scheduled outside Aug–Oct.
R-03	UX / Visual Designer (Bill)	1 person, 75% during design, 25% otherwise	Senior-level skill; familiar with WCAG 2.1 AA.	Heaviest load Jul–Aug for brand/visual design.
R-04	Content Strategist (Christine)	1 person, 60% throughout	Mid-level skill; firm voice and tone familiarity.	Long tail of content production Jul–Sep.
R-05	Frontend Contractor	1 vendor, ~60 hours	Available via firm's approved supplier list; Net 30 payment.	Supplements Bob during build phase.
R-06	Marketing Lead (SME, internal)	1 person, ~5% time	Available for design reviews and content approvals.	Functional manager; not under PM authority.
R-07	Sponsor (Mary)	1 person, ~3% time	Available for milestone reviews and brand sign-off.	Decision-maker only; not chargeable to project.
R-08	Legal / Compliance reviewer	1 person, ~10 hours total	Available for privacy, accessibility, vendor contract review.	On-call resource; flat-rate internal cost.
R-09	Cloud hosting environments	3 (dev, staging, prod)	Firm-approved provider; standard tier sufficient.	Provisioned in week 1 of build phase.
R-10	CMS license	1 group (5 editor seats)	Annual license; 5 seats covers Marketing team + admins.	License extends 12 months from go-live.
R-11	CI/CD pipeline access	1 project (firm-standard)	Existing firm tooling; no new license needed.	Bob configures pipeline for this project.
R-12	Analytics & tag manager	1 setup (Google Analytics + GTM)	Free tier sufficient for traffic levels.	Marketing Lead approves dashboard design.
R-13	Stock imagery library	~50 images	Royalty-free, commercial license; budget $2,200.	Bill curates; alt-text drafted for accessibility.
R-14	Photography session	1 day	External photographer; consultant headshots.	Subset of consultants only — not all 500.
R-15	WCAG 2.1 AA audit (3rd party)	1 audit cycle	Accredited firm; budget $4,000.	Awarded via competitive bid; 3 quotes obtained.
R-16	Design tools / fonts license	Existing firm seats + $400 fonts	Bill uses existing Figma/Adobe access.	Specialty fonts purchased for brand.
R-17	Office workspace (hybrid)	1 day/week in-person during build	Existing firm offices; no new facility needed.	Encouraged for design/dev hand-offs.

ID	Resource	Quantity	Assumptions	Comments
R-18	Meeting rooms	Booked as needed	Existing firm bookings via standard system.	Sponsor-review sessions need executive boardroom.

27

Risk Register

Repository of identified risks with analysis and response plans.

RISK REGISTER – IDENTIFICATION & INITIAL ANALYSIS

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	Updated Aug 15, 2026

Outputs from Identify Risks and Perform Qualitative Risk Analysis. Probability and Impact each scored 1–5; Score = P × max(Impact across objectives).

ID	Cat	Risk Statement	Owner	P	Impact (Sc/Qu/Sch/Co)				Score	Level	Response Strategy
					Sc	Qu	Sch	Co			
R-01	Technical	CRM API integration may be more complex than expected, delaying lead-form go-live.	Bob (Dev)	3	2	2	4	3	12	Med-High	Mitigate
R-02	Technical	WCAG 2.1 AA audit may surface Severity-1 findings late in the project, requiring rework.	Bill (UX)	3	1	5	3	3	15	High	Mitigate
R-03	External	Frontend contractor may be unavailable when needed, delaying frontend build.	Andrew (PM)	2	1	1	3	2	6	Low	Mitigate
R-04	Organizational	Sponsor (Mary) may delay design approval beyond planned 5-day window, slipping the design milestone (M04).	Andrew (PM)	4	1	1	4	2	16	Critical	Mitigate
R-05	Organizational	Consultants (500+) may not provide bios on time, delaying directory and content launch.	Christine	4	4	3	2	1	16	Critical	Mitigate
R-06	Organizational	Bob, Bill, or Christine may take an unplanned absence (illness, family) during build phase.	Andrew (PM)	2	1	2	4	3	8	Medium	Mitigate
R-07	External	Hosting / CMS vendor outage during cutover (A038) could prevent Go-Live.	Bob (Dev)	1	1	1	5	1	5	Low	Transfer / Mitigate
R-08	External	Legal/Compliance review may identify GDPR or privacy issues late, blocking launch.	Andrew (PM)	2	2	3	3	2	6	Low	Mitigate
R-09	Project Mgmt	Effort estimates for build activities (A024, A025) may be optimistic, exceeding the cost baseline.	Andrew (PM)	3	1	1	2	4	12	Med-High	Accept (active)
R-10	Technical	Site performance may not meet LCP < 2.5s target on image-heavy pages (case studies, directory).	Bob (Dev)	3	1	4	2	2	12	Med-High	Mitigate
R-11	Organizational	Marketing Lead may want to expand scope post-design approval (e.g., add a careers section).	Andrew (PM)	4	4	1	3	3	16	Critical	Mitigate
R-12	Organizational	FY2026 budget pressure could reduce the project's funding mid-stream.	Mary (Sponsor)	1	5	2	5	5	5	Low	Avoid (Sponsor-managed)
R-13	Project Mgmt	IT/Hosting Operations may not be ready to accept handoff at Go-Live, leaving the PM team holding production support.	Andrew (PM)	3	1	2	1	3	9	Medium	Mitigate
R-14	Opportunity	Consultants featured in case studies may proactively share the new site, providing free marketing reach.	Marketing Lead	4	1	1	1	-2	8	Medium	Enhance
R-15	Opportunity	WCAG 2.1 AA compliance may attract clients who require accessibility-compliant vendors (gov, healthcare, education).	Sales Lead	3	1	1	1	-3	9	Medium	Exploit

RISK REGISTER – RESPONSE PLAN & MONITORING

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	Updated Aug 15, 2026

Outputs from Plan Risk Responses and Monitor Risks. 'Residual Score' is the score after the response is implemented. Negative cost values denote opportunities (savings).

ID	Action Plan	Responsible Party	Trigger / Symptom	Resid. P	Resid. Score	Status	Comments
R-01	1. Schedule a 4-hour CRM-vendor technical call in week 1 of Build (Aug 17). 2. Build a parallel test harness against CRM sandbox. 3. If > 1-week delay risk, fall back to email-form submission with manual CRM entry for launch.	Bob (Dev) – primary; Marketing Lead secondary	API discovery during A025 reveals missing fields or undocumented behavior.	**2**	**4**	**Mitigating**	Vendor call booked Aug 18.
R-02	1. Build accessibility checks into the component library (A023). 2. Run automated a11y linting on every PR. 3. Conduct an internal accessibility review at A024 completion (Sep 30) — before the formal audit.	Bill (UX); Bob ensures linter in CI	Audit report identifies Sev-1 findings.	**2**	**4**	**Mitigating**	Internal pre-audit booked Oct 1.
R-03	1. Sign frontend SOW by July 1, 2026. 2. Identify a backup contractor from approved-supplier list (already done: Vendor X). 3. Pre-pay 25% to lock contractor schedule.	Andrew (PM); Procurement	Contractor declines or doesn't respond to SOW by Aug 5.	**1**	**2**	**Closed**	SOW signed June 28.
R-04	1. Pre-book a 2-hour design review on Mary's calendar for Aug 5 — confirmed with EA. 2. Send an executive summary preview 1 week in advance. 3. Bill presents in person; PM facilitates same-day decisions.	Andrew (PM)	> 5 business days elapse between design submission and Mary's response.	**2**	**4**	**Mitigating**	Calendar booked.
R-05	1. Mary sends a firm-wide kickoff email setting the expectation. 2. Provide a 10-minute self-service form (instead of an interview). 3. Tier the rollout: top 50 consultants at launch, remainder added in batches post-launch. 4. Recognition in case studies for early submitters.	Christine; supported by Mary's email	< 50% bio response rate by week 2 of A016.	**3**	**6**	**Mitigating**	Firm-wide email scheduled June 15.
R-06	1. Document architecture, design system, and content pipeline so anyone can pick up. 2. Cross-train: Bob shadows Bill on accessibility; Christine shadows Bill on content design. 3. Identify backup contractors who can be onboarded in ≤ 1 week.	Andrew (PM); each team member	Team member unavailable for > 5 consecutive business days.	**2**	**4**	**Mitigating**	Documentation in progress.
R-07	1. Contractually require 99.5% SLA from vendor. 2. Schedule cutover Tue–Thu (not Mon/Fri) to allow vendor support. 3. Document rollback to legacy site (DNS revert) tested in advance.	Bob (Dev); IT/Hosting Operations	Vendor status page shows incident on cutover day.	**1**	**2**	**Mitigating**	Cutover tentatively Tue Nov 24.
R-08	1. Engage Legal at requirements (A006) and design (A011) — before build. 2. Use the firm's standard cookie-consent / privacy-policy template. 3. Schedule a Legal sign-off 4 weeks before launch.	Andrew (PM); Legal	Legal flags any Sev-1 issue in the privacy review.	**1**	**1**	**Mitigating**	Legal joined kickoff.
R-09	1. Hold $15,000 contingency reserve specifically for this risk pool. 2. Track CPI weekly during build phase. 3. Trigger management reserve request if CPI < 0.9 for 2 consecutive weeks.	Andrew (PM)	EAC trends > BAC at any phase gate.	**3**	**6**	**Open**	Watch CPI weekly.
R-10	1. Implement image-CDN with auto-resize from build start. 2. Lazy-load all below-fold imagery. 3. Performance budget enforced in CI (fail build if LCP > 2.5s).	Bob (Dev)	Performance test (A030) shows 75th-percentile LCP > 2.5s.	**2**	**4**	**Mitigating**	CDN selected.

ID	Action Plan	Responsible Party	Trigger / Symptom	Resid. P	Resid. Score	Status	Comments
R-11	1. Documented scope-statement exclusions reviewed at Marketing kickoff. 2. Any scope-add goes through formal change-control (no exceptions). 3. Maintain a 'Phase 2 backlog' so good ideas have a home without disrupting Phase 1.	Andrew (PM); Marketing Lead	Any scope-add request from Marketing Lead post-M04.	**3**	**3**	**Mitigating**	Phase 2 backlog established.
R-12	1. Sponsor secured first-call on FY2026 funding. 2. Quarterly tranche release confirmed. 3. PM reports on benefits early to maintain executive support.	Mary (Sponsor)	CFO communicates budget reallocation.	**1**	**1**	**Closed**	Sponsor confirmed June 1.
R-13	1. Engage IT/Hosting Ops at architecture review (Aug 5). 2. Draft runbooks during build, not at end. 3. Joint cutover rehearsal Nov 17 (1 week before Go-Live).	Andrew (PM); IT/Hosting Operations	IT raises concerns about runbooks or monitoring in late October.	**2**	**2**	**Mitigating**	IT engaged at kickoff.
R-14	1. Provide pre-written social-share copy to featured consultants. 2. Recognize sharing leaders in the firm's all-hands meeting. 3. Track referral traffic in analytics.	Marketing Lead; Christine	Launch announcement.	**4**	**12**	**Open**	Social-share kit drafted.
R-15	1. Sales Lead develops WCAG-compliance messaging post-audit. 2. Landing page on the new site for accessibility-first prospects. 3. Add accessibility credentials to RFP responses.	Sales Lead; Marketing Lead	Audit pass + sales messaging update.	**3**	**12**	**Open**	Sales briefed.

28

Risk Report

Summary of overall project risk exposure and trend analysis.

RISK REPORT

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date Prepared: May 7, 2026

Overview of Overall Project Risk Exposure

As of the latest reporting period, overall project risk exposure is rated MODERATE. The Risk Register contains 14 active risks: 3 High, 6 Medium, and 5 Low. Total expected monetary value (EMV) of identified threats is approximately $11,500; EMV of identified opportunities is approximately $4,200. The Management Reserve of $10,000 is currently sufficient to absorb expected residual threat exposure.

Summary of Top Threats

1. CRM integration complexity (High) – HubSpot data model differs from legacy; mitigated by spike in Sprint 2.
2. Content delivery from Marketing (High) – dependency on external SME availability; mitigated with content calendar and backup writer.
3. Cybersecurity / data privacy (High) – external pen test scheduled in Phase 5; remediation budget reserved.
4. Browser compatibility on legacy IE/Edge (Medium) – scope confirmed: support last two versions only.
5. Stakeholder availability for UAT (Medium) – UAT window extended to 2 weeks; backup approvers identified.

Summary of Top Opportunities

1. Reusable component library (Medium) – building modular components could accelerate future client work; estimated savings $5K/project.
2. SEO uplift from new architecture (Low) – early indicators suggest organic traffic could grow 20% within 6 months post-launch.
3. AWS reserved-instance pricing (Low) – committing to 1-year reserved instances reduces hosting cost by ~25%.

Trend Analysis

Risk count has decreased from 19 at planning to 14 at most-recent review as design and build risks have been retired. Two new risks were added during integration. Overall risk trajectory is decreasing as the project moves toward launch.

Recommended Risk Responses Pending Approval

• Engage backup content writer (Threat #2) – $3,500, awaiting CCB approval.
• Lock 1-year AWS reserved instance (Opportunity #3) – $2,400 commitment, awaiting sponsor approval.
• Extend pen-test scope to include API endpoints – $1,500, recommended.

Reserve Status

• Contingency Reserve: $6,000 of $8,000 remaining (75%).
• Management Reserve: $10,000 of $10,000 remaining (100%).
• Reserves are sufficient to cover expected residual risk through Go-Live.

Conclusion

Overall project risk exposure is within tolerance. Active mitigation of the top three threats is on track. The PM (Andrew) and Sponsor (Mary) review this report monthly; next review scheduled per the Risk Management Plan.

29

Schedule Data

Supporting schedule data: histograms, cash flow, reserve, and assumptions.

SCHEDULE DATA

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Supporting schedule data including activity attributes used for scheduling calculations, resource histograms, cash-flow projections, and schedule reserves. Used in conjunction with the Project Schedule and Schedule Network Diagram.

Item	Detail
Schedule model used	Critical Path Method (CPM) with resource leveling
Tool	Microsoft Project + Jira (sprint backlog)
Total project duration	30 weeks (May 8, 2026 – Dec 31, 2026)
Critical path length	30 weeks
Critical path activities	Charter → Requirements → Design Approval → CMS Build → CRM Integration → System Test → UAT → Go-Live
Total float on critical path	0 days
Largest non-critical float	8 days (Content Development branch)
Schedule contingency reserve	10 working days (held by PM)
Management reserve (schedule)	5 working days (held by Sponsor)
Resource leveling adjustments	Bob shifted 2 days; Christine shifted 3 days; both within float
Calendars referenced	Project calendar (M-F, 8 hr/day, US holidays); Bob (US Central); Bill (Eastern)
Milestones (count)	10 major milestones (see Milestone List)
Number of activities	78 activities across 6 phases
Average activity duration	3.5 working days
Cash-flow profile	Front-loaded for design/build; tapers in test/launch (see Cost Baseline S-curve)
Last schedule update	Per latest weekly status report
Next baseline review	End of Phase 4 (Build complete)

30

Schedule Forecast

Forecast of project completion dates based on Schedule Performance.

SCHEDULE FORECAST

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date: May 7, 2026

Schedule forecast based on Earned Value Analysis. Estimate at Completion (time) is calculated using the Schedule Performance Index (SPI). Time-based EAC = Original Duration / SPI. Original duration: 30 weeks. Planned finish: Dec 31, 2026.

Reporting Period	PV	EV	SV	SPI	EAC (weeks)	Forecast Finish	Status
End of Month 1	$15,000	$14,000	-$1,000	0.93	32.2	Jan 14, 2027	2 wks late
End of Month 2	$30,000	$32,000	+$2,000	1.07	28.1	Dec 17, 2026	Ahead
End of Month 3	$58,000	$58,000	$0	1.00	30.0	Dec 31, 2026	On schedule
End of Month 4	$95,000	$92,000	-$3,000	0.97	31.0	Jan 7, 2027	1 wk late
End of Month 5	$128,000	$128,000	$0	1.00	30.0	Dec 31, 2026	On schedule
End of Month 6 (Forecast)	$144,000	$144,000	$0	1.00	30.0	Dec 31, 2026	On schedule

31

Stakeholder Register

Identified stakeholders, classification, and assessment information.

STAKEHOLDER REGISTER

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 6, 2026

Name	Position / Role	Contact Information	Requirements	Expectations	Classification
Mary	CEO / Project Sponsor	mary@marysconsulting.com	Brand-aligned site that reaches Fortune 500 buyers; stays within $150K budget; 6-month delivery.	Personal sign-off on visual brand; quarterly benefit reviews after launch.	High Power / High Interest – Manage Closely
Andrew	Project Manager	andrew@marysconsulting.com	Clear charter, decision authority within budget, engaged sponsor.	Successful delivery on scope, time, cost, quality.	High Power / High Interest – Manage Closely
Bob	Web Developer / Tech Lead	bob@marysconsulting.com	Approved tech stack, CMS choice, dev environment, CRM API access.	Clear specs and stable requirements once signed off.	Med Power / High Interest – Keep Informed
Bill	UX / Visual Designer	bill@marysconsulting.com	Brand guidelines, access to CEO for design reviews.	Reasonable rounds of design review with timely feedback.	Med Power / High Interest – Keep Informed
Christine	Content Strategist / Copywriter	christine@marysconsulting.com	Access to consultants for bios/case studies; brand voice guidance.	Realistic content deadlines; SME availability.	Med Power / High Interest – Keep Informed
Marketing Lead	Internal Marketing owner of the site post-launch	marketing.lead@marysconsulting.com	Editor-friendly CMS; lead routing to CRM; analytics dashboards.	Minimal IT dependency for content updates after launch.	High Power / High Interest – Manage Closely
Sales Lead	Recipient of inbound leads	sales.lead@marysconsulting.com	Qualified leads routed to the right consultants; RFP form data captured cleanly.	Increased pipeline quality and volume.	Med Power / High Interest – Keep Informed
Consultant Community (500+)	Global consultants providing bios and case studies	all-consultants@marysconsulting.com	Easy way to submit/update bios; recognition of their work in case studies.	Their content is accurately represented and kept up to date.	Low Power / Med Interest – Keep Informed
Fortune 500 Prospects	External target audience / end users of the site	Via sales / marketing channels	Credible firm presentation; clear service descriptions; easy contact path.	A professional, fast, and accessible website experience.	Low Power / Low Interest – Monitor
IT / Hosting Operations	Internal owners of post-launch hosting and support	it-ops@marysconsulting.com	Architecture meets IT standards; documented runbooks; security compliant.	Smooth handoff with monitoring and alerts in place.	High Power / Low Interest – Keep Satisfied
Legal / Compliance	Privacy, accessibility, and contract review	legal@marysconsulting.com	GDPR-compliant data handling, WCAG 2.1 AA compliance, vendor contracts reviewed.	Early involvement before public launch.	High Power / Low Interest – Keep Satisfied

Name	Position / Role	Contact Information	Requirements	Expectations	Classification
Hosting / CMS Vendor	External technology supplier	Via account manager	Clear specifications; SOW; payment per contract.	Predictable scope and on-time payment.	Low Power / Low Interest – Monitor

32

Team Charter

Team values, agreements, communication norms, and meeting guidelines.

TEAM CHARTER

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 18, 2026

Team Values and Principles

1.	**Respect** – We treat each other and our stakeholders with respect, even under deadline pressure.
2.	**Transparency** – We surface issues and risks early rather than hide them; bad news travels faster than good news on this team.
3.	**Quality** – We hold ourselves to a high bar; accessibility and security are non-negotiable, not optional polish.
4.	**Ownership** – Each team member owns their domain fully; the PM owns escalation, not micromanagement.
5.	**Continuous improvement** – We retro at the end of each phase and adjust how we work.

Meeting Guidelines

1.	Weekly team standup, Monday 9:30–10:00 AM, in-person or video.
2.	Sponsor steering, last Friday of each month, 30 minutes.
3.	Every meeting has a written agenda 24 hours in advance and a written outcome within 24 hours after.
4.	Camera-on default for video calls; turning off is fine when context calls for it.
5.	Decisions made in meetings are recorded in the Decision Log; if you're not in the room, you'll see it there.

Communication Guidelines

1.	Slack for fast sync; email for decisions and external stakeholders; ticket system for work tracking.
2.	Response expectations: Slack ≤ 4 business hours; email ≤ 1 business day; tickets ≤ 2 business days.
3.	After hours: no expectation of response. Mark urgent issues with @here only when truly urgent.
4.	When stuck for > 2 hours, ask. Heroes-in-silence is an anti-pattern on this team.
5.	PM is the single point of contact for sponsor and external-stakeholder communication unless explicitly delegated.

TEAM CHARTER

Project Title:	Mary's Consulting – New Company Website	Date Prepared:	May 18, 2026

Decision-Making Process

Within team domain: Each team member has authority to make decisions within their domain (Bob – tech, Bill – design, Christine – content) without PM approval, as long as the decision fits inside the approved scope, schedule, and budget.
Cross-domain: Decisions affecting multiple domains are surfaced to the PM and decided by team consensus when possible. PM has tie-breaker authority.
Outside scope/baseline: Decisions that change scope, schedule, or cost go through the formal change-control process and require sponsor approval per the PM Plan.
Decisions logged: All cross-domain or sponsor-level decisions are recorded in the Decision Log.

Conflict Resolution Process

Step 1 – Direct conversation: The team members involved attempt to resolve the conflict directly within 1 business day.
Step 2 – PM facilitation: If unresolved, the PM facilitates a discussion within 2 business days.
Step 3 – Sponsor escalation: Conflicts that affect scope, cost, schedule, or quality and cannot be resolved by the PM are escalated to the Sponsor.
Tone: Disagree with ideas, not people. Focus on what's best for the project, not on personal preferences.

Other Agreements

- **Working hours:** Core hours 10 AM – 3 PM ET; outside core hours, team members work flexibly.
- **Vacation:** Notify the team and PM at least 2 weeks in advance for vacations > 1 day.
- **On-call:** Bob is on-call during the 2-week hypercare window after launch; rotation arranged afterward.
- **Knowledge sharing:** All design and code stored in the firm's shared repositories; no personal-drive-only artifacts.
- **Charter is living:** This charter can be amended by team consensus and re-signed; review at each phase gate.

Signatures

Name / Role	Signature	Date
Andrew (PM)		May 18, 2026
Bob (Web Developer)		May 18, 2026
Bill (UX Designer)		May 18, 2026
Christine (Content Strategist)		May 18, 2026

33

Test and Evaluation Documents

Test plans, test cases, evaluation criteria, and verification activities.

TEST AND EVALUATION DOCUMENTS

Project: Mary's Consulting – New Company Website | PM: Andrew | Sponsor: Mary | Date Prepared: May 7, 2026

Purpose

This document summarizes the testing and evaluation artifacts used to verify that the Mary's Consulting website meets specified requirements before public launch.

Test Strategy

Multi-layer testing combining automated unit tests (developers), automated integration tests (CI pipeline), manual functional tests (QA), performance tests (Lighthouse + k6), security testing (external pen test), accessibility testing (axe-core + manual), and User Acceptance Testing led by the Marketing and IT leads on behalf of business stakeholders.

Test Environments

• Development (developer laptops): unit and component testing.
• Staging (AWS, mirror of production): full integration, performance, and UAT.
• Production (AWS): smoke testing only post-deploy.
• All environments use environment-specific configuration; no production data flows to lower environments.

Test Cases (Summary)

• Functional test cases: 124 (covering navigation, forms, search, CMS authoring, CRM lead capture).
• Integration test cases: 32 (CMS↔CRM, CMS↔Analytics, CDN, email gateway).
• Performance scenarios: 8 (homepage, services, contact form, search under load).
• Security tests: 25 OWASP Top-10 categories + custom checks.
• Accessibility checks: WCAG 2.1 AA across all template pages.

UAT Plan

• Duration: 2 weeks (Phase 5).
• Participants: 5 reviewers (Marketing Lead, IT Lead, 2 sales reps, 1 client services lead).
• Entry criteria: 100% functional tests passing on staging; 0 critical defects.
• Exit criteria: ≥ 95% UAT pass rate; 0 critical, ≤ 3 high defects open.
• Sign-off: Sponsor (Mary) signs Formal Acceptance form.

Defect Management

Defects logged in Jira; severity 1 (critical) addressed within 1 day, severity 2 (high) within 3 days, severity 3 (medium) within sprint, severity 4 (low) backlogged. Daily defect triage during test phase.

Evaluation Metrics

See Quality Control Measurements (document #19) for measured results against quality metrics. All metrics achieved target prior to Go-Live.

Test Artifacts (Stored in SharePoint)

• Test Plan v1.2
• Test Case Library (Excel) – 124 functional, 32 integration, 8 performance
• Pen-Test Report (External vendor) – delivered Phase 5
• UAT Sign-Off Sheets (5)
• Defect Reports (Jira export)
• Quality Control Measurements (document #19)
• Quality Audit (Quality_Audit.pdf)
