# STAKEHOLDER MAPPING – POWER / INTEREST GRID

| | | | |
|---|---|---|---|
| **Project Title:** | | **Date Prepared:** | |

*Plot each stakeholder by how much power they have over the project (vertical) and how much interest they have in its outcome (horizontal). The quadrant determines the engagement strategy.*

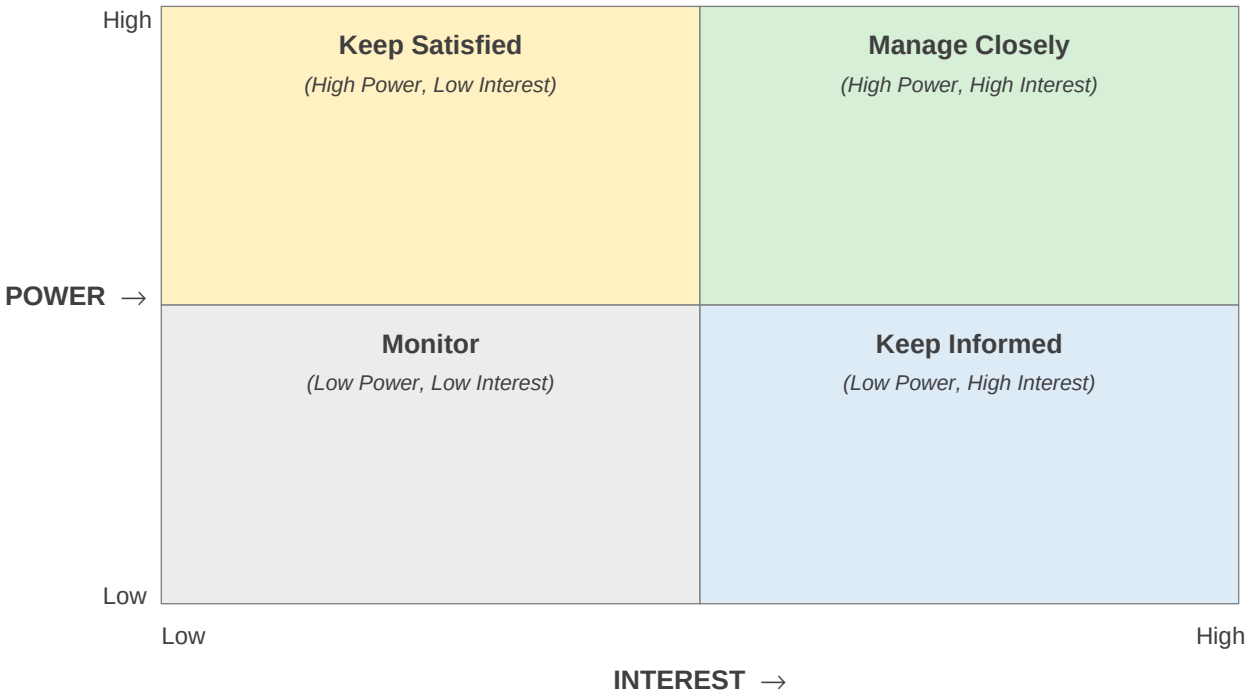


| | | | |
|---|---|---|---|
| **Manage Closely**<br>High Power, High Interest – actively engage, frequent communication. | **Keep Satisfied**<br>High Power, Low Interest – meet their needs but don't overload with detail. | **Keep Informed**<br>Low Power, High Interest – share progress and listen to feedback. | **Monitor**<br>Low Power, Low Interest – minimal communication; watch for changes. |

# STAKEHOLDER MAPPING – SALIENCE MODEL

| **Project Title:** | | **Date Prepared:** | |
|---|---|---|---|

*The Salience Model classifies stakeholders by the combination of three attributes: **Power** (ability to impose their will), **Urgency** (need for immediate attention), and **Legitimacy** (their involvement is appropriate). Stakeholders with all three attributes are the highest priority.*

| Category | Attributes | How to Engage | Stakeholders |
|---|---|---|---|
| **Definitive** | Power + Urgency + Legitimacy | Highest priority – act on their needs first. | |
| **Dominant** | Power + Legitimacy (no urgency) | Strong claim but not pressing – keep them satisfied. | |
| **Dependent** | Urgency + Legitimacy (no power) | Need PM advocacy because they cannot act alone. | |
| **Dangerous** | Power + Urgency (no legitimacy) | Coercive – manage carefully, may surface issues quickly. | |
| **Dormant** | Power only | Latent influence; communicate enough to stay aware. | |
| **Discretionary** | Legitimacy only | Worth informing; little immediate effect on the project. | |
| **Demanding** | Urgency only | Noisy but low influence – acknowledge, but do not over-invest. | |

# STAKEHOLDER MAPPING – DIRECTIONS OF INFLUENCE

| Project Title: | | Date Prepared: | |
|---|---|---|---|

*Classify stakeholders by the direction they influence the project relative to the project manager. This guides the communication style and channel for each group.*

| Direction | Description | Stakeholders |
|---|---|---|
| **Upward** | Senior leadership / sponsor influence | |
| **Downward** | Project team members reporting into the PM | |
| **Outward** | External: customers, vendors, regulators, public | |
| **Sideward** | Peers and other functional managers within the firm | |

| | |
|---|---|
| **UPWARD**<br>**Sponsor / Executives** | **SIDEWARD**<br>**Peer functional managers** |
| **DOWNWARD**<br>**Project team** | **OUTWARD**<br>**External stakeholders** |
